

PROJECT INITIATION REPORT

EA 4Y400

Operational Improvement; NAPA 121 PM 7.2 at Hennessy Drive in the City of Napa

Scope: Operational Improvement

EA 2Q510 - Nominated in 2026 SHOPP

Pavement Rehab; NAPA 29 PM 42.1/48.6 in County of Napa

Scope: Pavement rehabilitation and Safety Improvements

EA 0W750

Intersection Improvement; NAPA 29 PM 28.485 at Pope St. in the City of St. Helena

Scope: Intersection Improvement

EA 1X750

Garnett Creek Bridge Replacement; NAPA 29 PM 39.08 in the City of Calistoga

Scope: Bridge Replacement

EA 1X760 - Nominated in 2026 SHOPP

Garnett Creek Branch Bridge Replacement; NAPA 29 PM 38.96 near the City of Calistoga

Scope: Bridge Replacement

Target Delivery Year: FY 2032/2033

ENVIRONMENTAL

EA 2W880

Pavement Preservation; NAP 128 PM 4.56/19.10 in County of Napa from R29 to Knoxville Road

Scope: Pavement Preservation

Cost Estimate: \$27 M Construction Capital

Schedule: **PAED: 04/2027** **PS&E: 11/2028** **RWC: 12/2028** **RTL: 01/2029**

EA 4W370

Bridge Scour Mitigation; NAPA 29 PM 6.99 in County of Napa at the Napa River BOH (aka George Butler Bridge)

Scope: Scour Mitigation and Seismic Retrofit.

Cost Estimate: \$14.6 M Construction Capital

Schedule: **PAED: 10/2027** **PS&E: 4/2029** **RWC: 5/2029** **RTL: 7/2029**

EA 4Q010

NAPA 29 PM 0.6/R2.5 in City of American Canyon

Scope: Multi-Modal Corridor Improvements

Between Napa Junction Rd and American Canyon Rd

Cost Estimate: \$ 53.1 M Construction Capital

Schedule: **PSR/PDS: 2/6/2023** **PAED: 12/2026** **PS&E: 12/2027** **RWC: 6/2028** **RTL: 6/2028**

A PAED coop agreement is executed on 2/29/2024

PIR (Project Initiation Report)	PSR (Project Study Report)	DED (Draft Environmental Document)
PAED (Project Approval/ Environmental Document)		PSE (Plans, Specifications, and Estimate)
RWC (Right of Way Certification)	RTL (Ready to List)	CCA (Construction Contract Acceptance)
ADV (Advertise Contract)	BO (Bid Open)	AWD (Award Contract)

EA 0J890

5-Way Intersection; NAPA 121-PM 7.3 in City of Napa

Scope: Intersection Improvement

At the intersection of Rt 121, Third St, East Ave and Coombsville

Cost Estimate: \$34.95 M Construction Capital (\$3.90 M SHOPP Contribution)

Schedule: DED: 08/28/2025 **PAED: 8/2026** PS&E: 4/2028 RWC: 4/202 **RTL: 4/2028**

A coop agreement is executed on 8/28/2023

EA 0X110

Napa Valley Vine Trail Gap Closure; NAPA 29 PM 19.00/29.25 in County of Napa

Scope: Construct Class I & Class III Bicycle Facilities

From California Drive in the Town of Yountville to Pratt Ave

Cost Estimate: \$25.3 M Construction Capital

Schedule: DED: 09/2026 **PAED: 12/2026** PS&E: 2/202 RWC: 9/2027 **RTL: 11/2028**

DESIGN

EA 2W370

Major Damage; NAPA 29 PM 42.57 in County of Napa

Scope: Replace failed netting with new netting, remove debris, and install additional erosion control.

Cost Estimate: \$1.8 M Construction Capital

Schedule: PAED: 4/28/2025 **PS&E: 4/3/2026** **RWC: 4/6/2026** **RTL: 4/14/2026**

EA 4AA30

Storm Damage; NAPA 128 PM 12.5 in County of Napa

Scope: Storm Damage Restoration – Install Soil Nail Wall

Cost Estimate: \$5.3 M Construction Capital

Schedule: PAED: 12/18/2024 PS&E: 08/2026 **RWC: 10/2026** **RTL: 11/2026**

EA 0Q800

Major Damage; NAPA 121 PM 6.9/12.1 in County of Napa

Scope: Permanent Restoration; Inject grout at sinkhole and install drainage

Cost Estimate: 1 M Construction Capital

Schedule: PA&ED: 10/15/2024 **PS&E: 03/27/2026** **RWC: 03/30/2026** **RTL: 03/30/2026**

EA 0Q82A

Mitigation & Bio Monitoring for Storm Damage; NAPA 29 PM 11.6/13.0 in County of Napa

Scope: Environmental mitigation at Multiple Locations

Cost Estimate: 253K Construction Capital

Schedule: PS&E: 3/04/2026 RWC: 3/13/2026 **RTL: 4/10/2026**

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

EA 0Q79A

Mitigation & Bio Monitoring for Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$600 K Construction Capital

Schedule: PS&E: 4/2027 RWC: 6/2027 RTL: 6/2027

EA 4AC80

Pavement Rehab; NAPA 29 PM 0.0/7.0 in American Canyon & County of Napa

Scope: Pavement rehabilitation

Cost Estimate: \$18.91 M Construction Capital

Schedule: PAED: 6/28/2024 PS&E: 9/2026 RWC:10/2026 RTL: 11/2026

EA 4J820

Tulucay Creek Bridge Replacement; NAPA 121 PM 5.9 in City of Napa

Scope: Bridge Replacement

Cost Estimate: \$15.6M Construction Capital

Schedule: DED: 06/30/2022 PAED: 03/27/2023 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

EA 1Q620

Pavement Rehab; NAPA 121 PM 4.47/10.7 in City of Napa

Scope: Pavement repair.

Cost Estimate: \$39.6 M Construction Capital

Schedule: PAED: 06/30/2022 PS&E: 06/2027 RWC: 08/2027 RTL: 08/2027

EA 2J88U

No-Name Creek Bridge: NAPA 29-PM 42.83 in County of Napa

Scope: Sub-structure rehabilitation and scour mitigation at one bridge

Cost Estimate: \$2.20M Construction Capital

Schedule: PAED: 2/1/2019 PS&E: 10/09/2025 RWC: 10//09/2025 RTL: 10/13/2025 AWD: 11/2026 AC: 12/2026

EA 4J830

Hopper Slough Creek; NAPA 128 PM 5.1 in County of Napa

Scope: Bridge Replacement

Cost Estimate: 12.2 M Construction Capital

Schedule: DED: 03/18/2022 PAED: 06/29/2022 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

EA 2W430

Napa Forward Intersection Improvements; NAPA 29 PM 22.72 in County of Napa

Scope: Operational and Safety Improvements at the intersection of Oakville Cross Rd and Rutherford Rd

Cost Estimate: \$8.5 M Construction Capital

Schedule: DED: 01/31/2024 PAED: 05/16/2025 PS&E: 06/2026 RWC: 07/2026 RTL: 07/2026

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

EA 4W940

Devlin/ Soscol Ferry Roundabout; NAPA 221-PM 0.00 in County of Napa

Scope: Construct Roundabout (DEER – Oversight by Napa County)

Cost Estimate: \$4.057M Construction Capital

Schedule: PS&E: 07/16/2025 RWC: N/A RTL: Pending Napa County Submission of Encroachment Permit

CONSTRUCTION

EA 0K63A

Plant Establishment and Environmental Mitigation; NAPA 29 PM 1.7/PM 5.1 in County of Napa

Scope: Plant establishment and environmental mitigation and monitoring work for bridge rail upgrade EA 0K630 In and near Yountville, at Dry Creek Bridge, Perfume Creek Bridge and California Drive UC.

Cost Estimate: \$0.31 M Construction Capital

Schedule: PS&E: 03/18/2025 RWC: 04/02/2025 RTL: 04/21/2025 AC: 02/27/2026 CCA: 6/2028

EA 4AC90

Safety; Various Locations in County of Napa

Scope: Install/ Upgrade Horizontal Alignment Warning Signs

Cost Estimate: \$4.47 M Construction Capital

Schedule: PAED: 6/21/2024 PS&E: 6/20/2025 RWC: 6/20/2025 RTL: 6/25/2025 AC: 12/30/2025 CCA: 12/2026

EA 0Q790

Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$2.4 M Construction Capital

Schedule: PAED: 02/9/2023 PS&E: 04/16/2025 RWC: 04/24/2025 RTL: 05/05/2025 AC: 11/18/2025 CCA: 12/2027

EA 4J411

Mitigation and Bio monitoring; NAPA 29 PM 1.7/PM 5.1 in American Canyon

Scope: Plant establishment and monitoring work for drainage improvement EA 4J410 at Rio Del Mar

Cost Estimate: \$0.60 M Construction Capital

Schedule: PS&E: 02/4/2025 RWC: 02/11/2025 RTL: 04/9/2025 AC: 11/26/2025 CCA: 12/2035

EA 2Q610

Pavement Rehab; NAPA 29 PM R7.3/13.5 in County of Napa

Scope: Pavement rehabilitation.

Cost Estimate: \$23.3M Construction Capital

Schedule: PAED: 04/20/2022 PS&E: 04/23/2024 RWC: 04/24/2024 RTL: 05/03/2024 AC: 11/26/2024 CCA: 10/2026

Awarded Contractor: Granite Rock Company

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

EA 0Q820

Storm Damage; NAPA 29 PM 11.6/13.0 in City of Napa

Scope: Repair Culvert and stabilize the roadway at Lincoln Ave

Cost Estimate: \$24.475M Construction Capital

Schedule: PAED: 09/10/2021 PS&E: 11/2023 RWC: 11/2023 RTL: 12/2023 AC: 10/2024 CCA: 12/2027

EA 0Q830

Storm Damage; NAPA 29 PM 46.1 in County of Napa

Scope: Construct CIDH segmented pile wall at slip out

Cost Estimate: \$1.7M Construction Capital

Schedule: PAED: 06/29/2022 RWC:1/11/2024 RTL: 1/22/2024 AC: 07/12/2024 CCA: 03/20/2026 EP: 9/2027

EA 3Q760

Rumble Strips; NAPA 29, 121 & 128 Various Locations in County of Napa

Scope: Construct rumble strips at seven locations.

Cost Estimate: \$3.3M Construction Capital

Schedule: PAED: 12/31/2021 RTL: 6/26/2023 AWD: 2/29/2024 AC: 03/27/2024 CCA 12/31/2024 EP: 12/2026

EA 0K630

Bridge Rails; NAPA 29 PM 16.48/19.04 in County of Napa

Scope: Upgrade / Replace Bridge Rails in 3 Bridges

Cost Estimate: \$4.7M Construction Capital

Schedule: PAED:10/22/2020 RWC:12/05/2022 RTL:12/05/2022 AC: 07/14/2023 CCA: 02/02/2026 EP: 04/2027

EA 0Q810

Storm Damage; NAPA 121 PM 16.0/16.1 in County of Napa

Scope: Repair pavement, replace drainage systems and upgrade guardrail.

Cost Estimate: \$1.3M Construction Capital

Schedule: PAED: 02/02/2022 RTL: 06/26/2023 AWD: 12/29/2023 AC: 1/23/2024 CCA:12/2/2024 EP: 05/2026

Awarded Contractor: Argonaut Constructors

EA 4J410

Drainage Improvement; NAPA 29 PM 1.7/5.1 in City of American Canyon

Scope: Rehabilitate Culverts

Cost Estimate: \$3.3M Construction Capital

Schedule: PAED: 2/4/2020 RTL: 10/3/2022 AWD: 3/21/2023 AC: 04/07/2023 CCA: 11/2025 EP: 12/2028

Awarded Contractor: Terracon Constructors Inc.

EA 0Q690

Storm Damage; NAPA 12 PM 2.1/2.6 in County of Napa

Scope: Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair

Cost Estimate: \$1.2M Construction Capital

Schedule: PAED:12/1/2020 RTL: 06/24/2022 AWD: 3/21/2023 AC: 03/03/2023 CCA: 10/30/2024 EP: 12/2026

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

EA 1G43A

Env. Mitigation at Conn Creek; NAPA 128 PM R7.4 on Silverado Trail in County of Napa

Scope: Environmental mitigation, monitoring and report at Conn Creek

Cost Estimate: \$0.2M Construction Capital

Schedule: PAED: 10/5/2015 PS&E: 6/28/2021 RWC: 08/10/2021 RTL: 08/23/2021 AC: 07/26/2022 CCA: 10/2031

EA 28120

Soscol Junction Improvement; NAPA 29 PM 5.0/7.1 and NAPA 221 PM 0.0/0.7 in County of Napa

Scope: Construct New Interchange at SR 221/29/12

Cost Estimate: \$36.7M Construction Capital

Schedule: PAED: 2/13/2020 PSE: 08/26/2021 RWC: 08/25/2021 RTL: 08/26/21 AC: 05/13/2022 CCA: 11/2026

EA 2Q260

Napa Valley Vine Trail; NAPA 29-PM 33.4/37.9 in County of Napa

Scope: Construct Class 1 Multiuse Path

Cost Estimate: \$13.2M Construction Capital

Schedule: DED: 6/17/2020 PAED: 01/15/2021 PS&E: 12/10/2021 RWC: 12/10/2021 RTL: 12/10/2021

AWD: 5/20/2022 (Ghilotti Construction Company) AC: 06/15/2022 CCA: 02/27/2026

EA 3G64A

Env. Mitigation & Plant Establishment at Napa River Bridge; NAPA 29 PM 37.0 in City of Calistoga

Scope: Environmental mitigation at Napa River Bridge

Cost Estimate: \$0.5M Construction Capital

Schedule: PAED: 2/9/2015 RTL: 5/29/2019 AWD: 3/26/2020 (Hanford Applied) AC: 05/28/2020 CCA: 12/2028

EA 4G210

Widen Roadway at Huichica Creek; NAPA 121-PM 0.75 in County of Napa

Scope: Remove existing triple box culverts and replace with a new single span bridge

Cost Estimate: \$8.7M Construction Capital

Schedule: PAED: 4/9/2018 RTL: 12/8/2020 AWD: 5/19/2021 (Gordon Ball Inc) CCA: 04/30/2024 EP: 09/2026

EA 4G21A

Env. Mitigation at Huichica Creek; NAPA 121-PM 0.75 in County of Napa

Scope: Environmental mitigation, monitoring and report at Huichica Creek

Cost Estimate: \$1.0M Construction Capital

Schedule: PAED: 4/9/2018 RTL: 06/9/2023 AWD: 11/28/2023 AC: 12/20/2023 CCA: 06/2033

EA 4G84A

Capell Creek Bridge Env Mitigation; NAPA 128-PM 20.2 in County of Napa

Scope: Environmental Permit Mitigation & Plant Establishment to Bridge Replacement

Cost Estimate: \$0.5M Construction Capital

Schedule: PAED: 6/16/2016 RTL: 05/23/2022 AWD: 11/17/2022 CCA: 11/2031

ACTION ITEMS

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)


CCA (Construction Contract Acceptance)

AWD (Award Contract)




Caltrans District 4 Active Projects in Napa County

May 2026

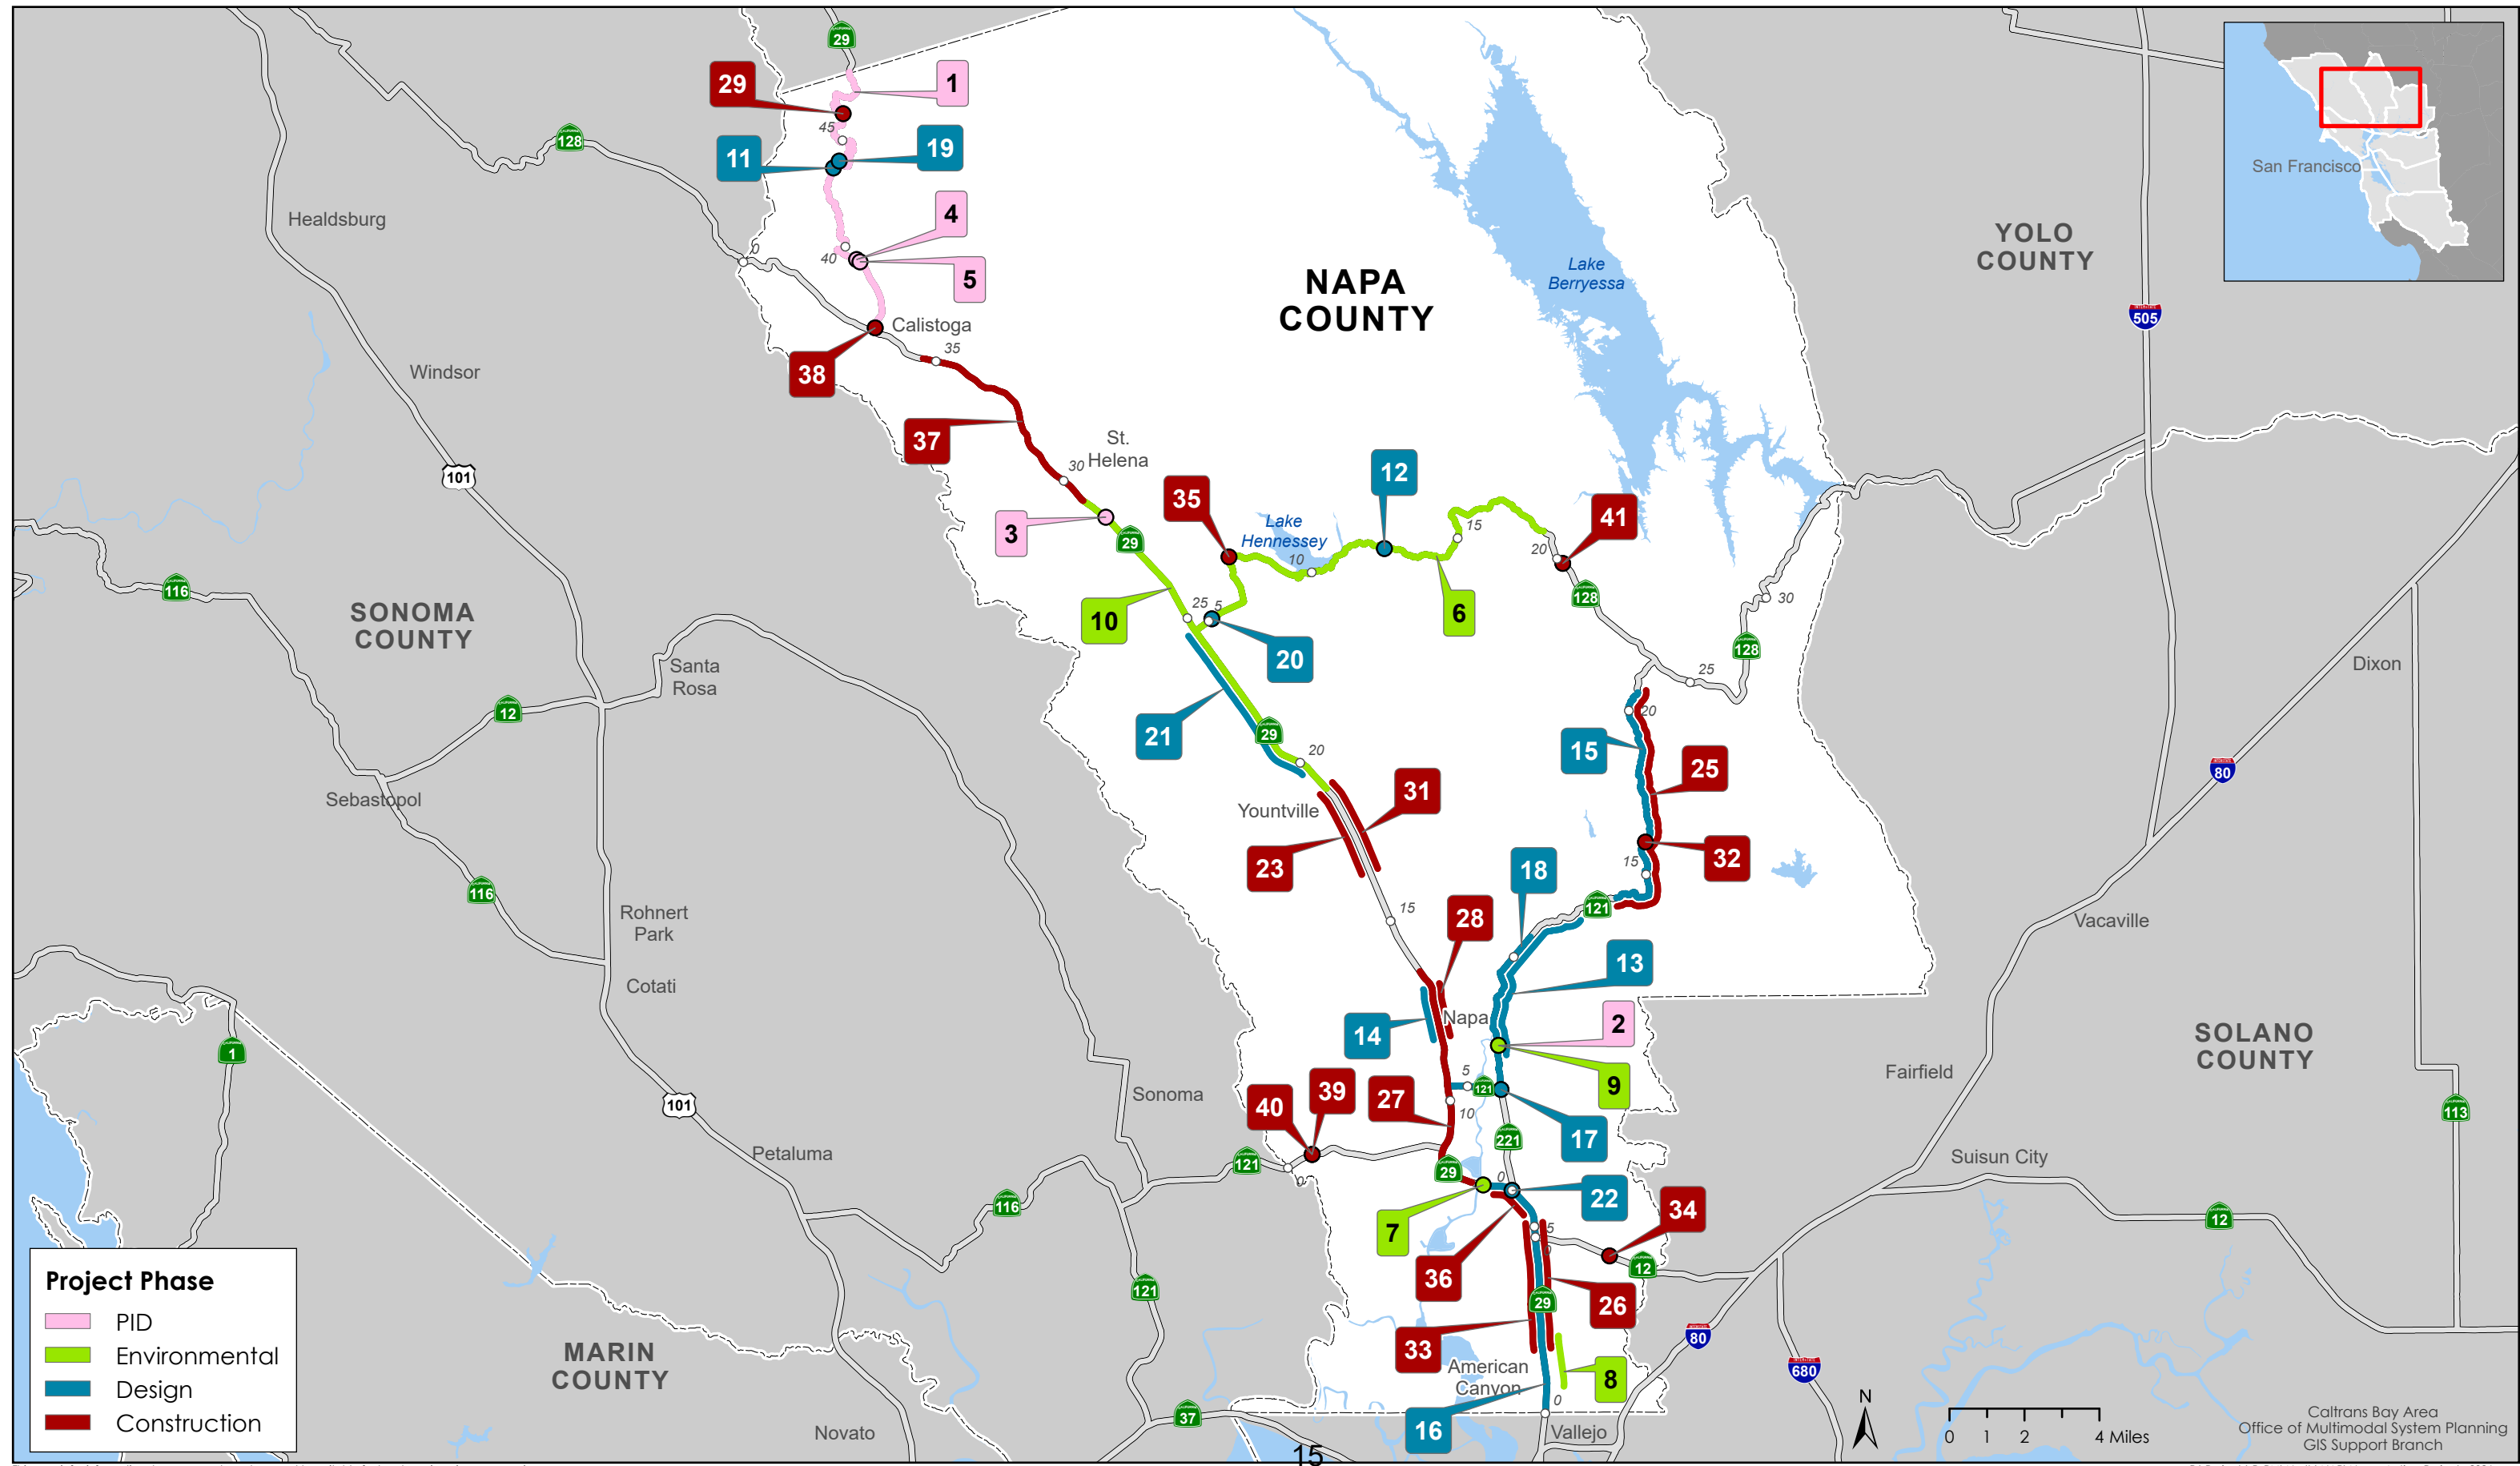

Project Phase

- PID
- Environmental
- Design
- Construction



Caltrans Bay Area
Office of Multimodal System Planning
GIS Support Branch

This map is for informational purposes only and may not be suitable for legal, engineering, or surveying purposes.

R:\Projects\VP_PM\North\NAPA\Napa_Active_Projects_2026.aprx

Caltrans District 4 Active Projects in Napa County - May 2026

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
1	PID	2Q510	29	36.8/48.6	Pavement rehabilitation	TBD	TBD	05/2030	12/2030	05/2031
2	PID	4Y400	121	7.2/7.2	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
3	PID	0W750	29	28.485/28.485	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
4	PID	1X750	29	39.08	Garnett Creek Bridge Replacement	TBD	TBD	TBD	TBD	TBD
5	PID	1X760	29	38.96	Garnett Creek Branch Bridge Replacement	\$18.1M	10/2029	10/2032	04/2033	12/2034
6	Environmental	2W880	128	4.56/19.1	Napa City Pavement Preservation	\$27.0M	04/2027	01/2029	07/2029	11/2031
7	Environmental	4W370	29	6.99/6.99	Bridge Scour Mitigation	\$14.6M	10/2027	07/2029	01/2030	01/2031
8	Environmental	4Q010	29	0.69/R2.054	Multi-Modal Corridor Improvements	\$53.1M	07/2026	06/2028	01/2029	06/2030
9	Environmental	0J890	121	7.20/7.40	Intersection Improvement	\$18.0 M (\$1.0M SHOPP Contribution)	8/1/2026	4/30/2028	12/1/2028	12/2030
10	Environmental	0X110	29	19.00/29.25	Napa Valley Vine Trail gap closure project	\$25.3M	05/2026	11/2028	05/2028	07/2029
11	Design	2W370	29	42.57	Replace failed netting with new netting, remove debris, and install additional erosion control.	\$1.8M	4/28/2025	04/14/2026	02/2027	05/2028
12	Design	4AA30	128	12.5	Storm Damage Restoration	\$5.3M	12/18/2024	11/2026	05/2027	06/2028
13	Design	0Q800	121	6.9/12.1	Permanent Restoration; Inject grout at sinkhole and install drainage	\$997K	10/15/2024	03/30/2026	12/2026	12/2027
14	Design	0Q82A	29	11.6/13	Lincoln Ave Mitigation & Bio Monitoring	\$253K	N/A	04/10/2026	10/2026	09/2030
15	Design	0Q79A	121	13.4/20.7	Env Mitigation for 0Q790	\$600K	N/A	06/2027	12/2027	12/2036
16	Design	4AC80	29	0.0/7.0	Pavement rehabilitation	\$18.9M	6/28/2024	11/2026	06/2027	01/2028
17	Design	4J820	121	5.9	Bridge Replacement	\$15.6M	3/27/2023	08/2028	02/2029	12/2030
18	Design	1Q620	121	4.47/10.7	Pavement repair	\$35M	6/30/2022	08/2027	03/2028	06/2029
19	Design	2J88U	29	42.83	Sub-structure rehabilitation and-One Bridge scour mitigation	\$2.2M	2/1/2019	10/13/2025	12/2026	12/2028
20	Design	4J830	128	5.1	Bridge Replacement	\$12.2M	6/29/2022	08/2027	02/2028	12/2030
21	Design	2W430	29	19.70/24.60	Operational and Safety Improvements	\$8.55M	5/16/2025	07/2026	09/2026	08/2028
22	Design	4W940	221	0	Devlin/ Soscol Ferry Roundabout	\$4.057M	12/17/2021	01/2026	05/2026	10/2027
23	Construction	0K63A	29	16.5/19.00	Plant Establishment and Environmental Mitigation	\$265K	N/A	4/21/2025	10/2025	06/2028
24(Not mapped)	Construction	4AC90	VAR	Var	Install/ Upgrade Horizontal Alignment Warning Signs	\$5.56M	6/21/2024	06/2025	12/2025	04/2028
25	Construction	0Q790	121	13.37/20.73	Construct RSP at five slipout locations.	\$6.4M	2/9/2023	5/5/2025	11/2025	12/2027
26	Construction	4J411	29	1.7/5.1	Sheehy Xrk Plant Mitigation	\$596K	N/A	4/9/2025	11/26/2025	12/2035
27	Construction	2Q610	29	R7.3/13.5	Pavement rehabilitation.	\$23.3M	4/20/2022	5/3/2024	11/27/2024	11/2026
28	Construction	0Q820	29	11.6/13.0	Repair Culvert and stabilize the roadway.	\$24.47M	9/10/2021	12/4/2023	10/1/2024	12/2026
29	Construction	0Q830	29	46.1	Construct CIDH segmented pile wall at slipout	\$1.7M	6/29/2022	1/22/2024	7/12/2024	03/20/2026
30(Not mapped)	Construction	3Q760	29	Var	Construct rumble strips at seven locations.	\$3.3M	12/31/2021	6/26/2023	3/27/2024	12/31/2024
31	Construction	0K630	29	16.48/19.04	Upgrade / Replace Bridge Rails	\$4.7M	10/22/2020	12/5/2022	7/14/2023	11/2025
32	Construction	0Q810	121	16.0/16.1	Repair pavement, replace drainage systems and upgrade guardrail.	\$1.3M	2/2/2022	6/26/2023	1/23/2024	12/2/2024
33	Construction	4J410	29	1.7/5.1	Rehabilitate Culverts	\$3.3M	2/4/2020	10/3/2022	4/7/2023	11/2025
34	Construction	0Q690	12	2.1/2.6	Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair	\$1.2M	12/1/2020	6/24/2022	3/3/2023	10/30/2024
35	Construction	1G43A	128	R7.4	Environmental mitigation, monitoring and report at Conn Creek	\$0.2M	10/5/2015	8/23/2021	7/26/2022	10/2031
36	Construction	28120	29	5.45/R6.7	Construct New Interchange at SR 221/29/12	\$36.7M	2/13/2020	8/26/2021	5/13/2022	11/2026
37	Construction	2Q260	29	29.24/35.34	Construct Class 1 Multiuse Path	13.2M	11/6/2020	12/10/2021	6/15/2022	10/2025
38	Construction	3G64A	29	37.0	Environmental mitigation at Napa River Bridge	\$0.5M	2/9/2015	5/29/2019	5/28/2020	12/2028

Caltrans District 4 Active Projects in Napa County - May 2026

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
39	Construction	4G210	121	0.75	Remove existing triple box culverts and replace with a new single span bridge	\$8.7M	4/9/2018	12/8/2020	6/10/2021	4/30/2024
40	Construction	4G21A	121	0.75	Environmental mitigation, monitoring and report at Huichica Creek	\$1M	4/9/2018	6/9/2023	12/20/2023	6/30/2033
41	Construction	4G84A	128	20.2	Environmental Permit Mitigation & Plant Establishment to Bridge Replacement	\$0.5M	6/16/2016	5/23/2022	12/21/2022	11/17/2031
