

**PROJECT INITIATION REPORT**

**EA 4Y400**

**Operational Improvement; NAPA 121 PM 7.2 at Hennessy Drive in the City of Napa**

Scope: Operational Improvement

**EA 2Q510 - Nominated in 2026 SHOPP**

**Pavement Rehab; NAPA 29 PM 42.1/48.6 in County of Napa**

Scope: Pavement rehabilitation and Safety Improvements

**EA 0W750**

**Intersection Improvement; NAPA 29 PM 28.485 at Pope St. in the City of St. Helena**

Scope: Intersection Improvement

**EA 1X750**

**Garnett Creek Bridge Replacement; NAPA 29 PM 39.08 in the City of Calistoga**

Scope: Bridge Replacement

**EA 1X760 - Nominated in 2026 SHOPP**

**Garnett Creek Branch Bridge Replacement; NAPA 29 PM 38.96 near the City of Calistoga**

Scope: Bridge Replacement

Target Delivery Year: FY 2032/2033

**ENVIRONMENTAL**

**EA 2W880**

**Pavement Preservation; NAP 128 PM 4.56/19.10 in County of Napa from R29 to Knoxville Road**

Scope: Pavement Preservation

Cost Estimate: \$13.8 M Construction Capital

Schedule: PAED: 10/2026      PS&E: 01/2028      RWC: 4/2028      RTL: 5/2028

**EA 4W370**

**Bridge Scour Mitigation; NAPA 29 PM 6.99 in County of Napa at the Napa River BOH (aka George Butler Bridge)**

Scope: Scour Mitigation and Seismic Retrofit.

Cost Estimate: \$14.6 M Construction Capital

Schedule: PAED: 10/2027      PS&E: 4/2029      RWC: 5/2029      RTL: 7/2029

**EA 4Q010**

**NAPA 29 PM 0.6/R2.5 in City of American Canyon**

Scope: Multi-Modal Corridor Improvements

Between Napa Junction Rd and American Canyon Rd

Cost Estimate: \$ 53.1 M Construction Capital

Schedule: PSR/PDS: 2/6/2023      PAED: 12/2026      PS&E: 12/2027      RWC: 6/2028      RTL: 6/2028

A PAED coop agreement is executed on 2/29/2024

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0J890**

**5-Way Intersection; NAPA 121-PM 7.3 in City of Napa**

**Scope:** Intersection Improvement

At the intersection of Rt 121, Third St, East Ave and Coombsville

**Cost Estimate:** \$34.95 M Construction Capital (\$3.90 M SHOPP Contribution)

**Schedule: DED:** 08/28/2025    **PAED:** 5/2026    **PS&E:** 4/2028    **RWC:** 4/202    **RTL:** 4/2028

A coop agreement is executed on 8/28/2023

**EA 0X110**

**Napa Valley Vine Trail Gap Closure; NAPA 29 PM 19.00/29.25 in County of Napa**

**Scope:** Construct Class I & Class III Bicycle Facilities

From California Drive in the Town of Yountville to Pratt Ave

**Cost Estimate:** \$25.3 M Construction Capital

**Schedule: DED:** 09/2026    **PAED:** 12/2026    **PS&E:** 2/202    **RWC:** 9/2027    **RTL:** 11/2027

**DESIGN**

**EA 2W370**

**Major Damage; NAPA 29 PM 42.57 in County of Napa**

**Scope:** Replace failed netting with new netting, remove debris, and install additional erosion control.

**Cost Estimate:** \$1.8 M Construction Capital

**Schedule: PAED:** 4/28/2025    **PS&E:** 3/2026    **RWC:** 3/2026    **RTL:** 4/2026

**EA 4AA30**

**Storm Damage; NAPA 128 PM 12.5 in County of Napa**

**Scope:** Storm Damage Restoration – Install Soil Nail Wall

**Cost Estimate:** \$5.3 M Construction Capital

**Schedule: PAED:** 12/18/2024    **PS&E:** 08/2026    **RWC:** 9/2026    **RTL:** 10/2026

**EA 0Q800**

**Major Damage; NAPA 121 PM 6.9/12.1 in County of Napa**

**Scope:** Permanent Restoration; Inject grout at sinkhole and install drainage

**Cost Estimate:** 1 M Construction Capital

**Schedule: PA&ED:** 10/2024    **PS&E:** 03/2026    **RWC:** 03/2026    **RTL:** 04/2026

**EA 0Q82A**

**Mitigation & Bio Monitoring for Storm Damage; NAPA 29 PM 11.6/13.0 in County of Napa**

**Scope:** Environmental mitigation at Multiple Locations

**Cost Estimate:** 253K Construction Capital

**Schedule: PS&E:** 3/04/2026    **RWC:** 3/13/2026    **RTL:** 5/2026

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0Q79A**

**Mitigation & Bio Monitoring for Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$600 K Construction Capital

Schedule: PS&E: 4/2027 RWC: 6/2027 RTL: 6/2027

**EA 4AC80**

**Pavement Rehab; NAPA 29 PM 0.0/7.0 in American Canyon & County of Napa**

Scope: Pavement rehabilitation

Cost Estimate: \$18.91 M Construction Capital

Schedule: PAED: 6/28/2024 PS&E: 9/2026 RWC:10/2026 RTL: 11/2026

**EA 4J820**

**Tuluca Creek Bridge Replacement; NAPA 121 PM 5.9 in City of Napa**

Scope: Bridge Replacement

Cost Estimate: \$15.6M Construction Capital

Schedule: DED: 06/30/2022 PAED: 03/27/2023 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

**EA 1Q620**

**Pavement Rehab; NAPA 121 PM 4.47/10.7 in City of Napa**

Scope: Pavement repair.

Cost Estimate: \$39.6 M Construction Capital

Schedule: PAED: 06/30/2022 PS&E: 06/2027 RWC: 08/2027 RTL: 08/2027

**EA 2J88U**

**No-Name Creek Bridge: NAPA 29-PM 42.83 in County of Napa**

Scope: Sub-structure rehabilitation and scour mitigation at one bridge

Cost Estimate: \$2.20M Construction Capital

Schedule: PAED: 2/1/2019 PS&E: 10/09/2025 RWC: 10/09/2025 RTL: 10/13/2025 AWD: 11/2026 AC: 12/2026

**EA 4J830**

**Hopper Slough Creek; NAPA 128 PM 5.1 in County of Napa**

Scope: Bridge Replacement

Cost Estimate: 12.2 M Construction Capital

Schedule: DED: 03/18/2022 PAED: 06/29/2022 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

**EA 2W430**

**Napa Forward Intersection Improvements; NAPA 29 PM 22.72 in County of Napa**

Scope: Operational and Safety Improvements at the intersection of Oakville Cross Rd and Rutherford Rd

Cost Estimate: \$8.5 M Construction Capital

Schedule: DED: 01/31/2024 PAED: 05/16/2025 PS&E: 06/2026 RWC: 07/2026 RTL: 07/2026

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 4W940**

**Devlin/ Soscol Ferry Roundabout; NAPA 221-PM 0.00 in County of Napa**

**Scope:** Construct Roundabout (DEER – Oversight by Napa County)

**Cost Estimate:** \$4.057M Construction Capital

**Schedule:** PS&E: 07/16/2025 RWC: N/A RTL: Pending Napa County Submission of Encroachment Permit

**CONSTRUCTION**

**EA 0K63A**

**Plant Establishment and Environmental Mitigation; NAPA 29 PM 1.7/PM 5.1 in County of Napa**

**Scope:** Plant establishment and environmental mitigation and monitoring work for bridge rail upgrade EA 0K630 In and near Yountville, at Dry Creek Bridge, Perfume Creek Bridge and California Drive UC.

**Cost Estimate:** \$0.31 M Construction Capital

**Schedule:** PS&E: 03/18/2025 RWC: 04/02/2025 RTL: 04/21/2025 AC: 02/27/2026 CCA: 6/2028

**EA 4AC90**

**Safety; Various Locations in County of Napa**

**Scope:** Install/ Upgrade Horizontal Alignment Warning Signs

**Cost Estimate:** \$4.47 M Construction Capital

**Schedule:** PAED: 6/21/2024 PS&E: 6/20/2025 RWC: 6/20/2025 RTL: 6/25/2025 AC: 12/30/2025 CCA: 12/2026

**EA 0Q790**

**Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

**Scope:** Construct RSP at five slip-out locations.

**Cost Estimate:** \$2.4 M Construction Capital

**Schedule:** PAED: 02/9/2023 PS&E: 04/16/2025 RWC: 04/24/2025 RTL: 05/05/2025 AC: 11/18/2025 CCA: 12/2027

**EA 4J411**

**Mitigation and Bio monitoring; NAPA 29 PM 1.7/PM 5.1 in American Canyon**

**Scope:** Plant establishment and monitoring work for drainage improvement EA 4J410 at Rio Del Mar

**Cost Estimate:** \$0.60 M Construction Capital

**Schedule:** PS&E: 02/4/2025 RWC: 02/11/2025 RTL: 04/9/2025 AC: 11/26/2025 CCA: 12/2035

**EA 2Q610**

**Pavement Rehab; NAPA 29 PM R7.3/13.5 in County of Napa**

**Scope:** Pavement rehabilitation.

**Cost Estimate:** \$23.3M Construction Capital

**Schedule:** PAED: 04/20/2022 PS&E: 04/23/2024 RWC: 04/24/2024 RTL: 05/03/2024 AC: 11/26/2024 CCA: 10/2026

**Awarded Contractor:** Granite Rock Company

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0Q820**

**Storm Damage; NAPA 29 PM 11.6/13.0 in City of Napa**

**Scope:** Repair Culvert and stabilize the roadway at Lincoln Ave

**Cost Estimate:** \$24.475M Construction Capital

**Schedule:** PAED: 09/10/2021 PS&E: 11/2023 RWC: 11/2023 RTL: 12/2023 AC: 10/2024 CCA: 12/2027

**EA 0Q830**

**Storm Damage; NAPA 29 PM 46.1 in County of Napa**

**Scope:** Construct CIDH segmented pile wall at slip out

**Cost Estimate:** \$1.7M Construction Capital

**Schedule:** PAED: 06/29/2022 PS&E: 1/11/2024 RWC:1/11/2024 RTL: 1/22/2024 AC: 07/12/2024 CCA: 04/2026

**EA 3Q760**

**Rumble Strips; NAPA 29, 121 & 128 Various Locations in County of Napa**

**Scope:** Construct rumble strips at seven locations.

**Cost Estimate:** \$3.3M Construction Capital

**Schedule:** PAED: 12/31/2021 RTL: 6/26/2023 AWD: 2/29/2024 AC: 03/27/2024 CCA 12/31/2024 EP: 12/2026

**EA 0K630**

**Bridge Rails; NAPA 29 PM 16.48/19.04 in County of Napa**

**Scope:** Upgrade / Replace Bridge Rails in 3 Bridges

**Cost Estimate:** \$4.7M Construction Capital

**Schedule:** PAED:10/22/2020 RWC:12/05/2022 RTL:12/05/2022 AC: 07/14/2023 CCA: 02/02/2026 EP: 04/2027

**EA 0Q810**

**Storm Damage; NAPA 121 PM 16.0/16.1 in County of Napa**

**Scope:** Repair pavement, replace drainage systems and upgrade guardrail.

**Cost Estimate:** \$1.3M Construction Capital

**Schedule:** PAED: 02/02/2022 RTL: 06/26/2023 AWD: 12/29/2023 AC: 1/23/2024 CCA:12/2/2024 EP: 04/2026

**Awarded Contractor:** Argonaut Constructors

**EA 4J410**

**Drainage Improvement; NAPA 29 PM 1.7/5.1 in City of American Canyon**

**Scope:** Rehabilitate Culverts

**Cost Estimate:** \$3.3M Construction Capital

**Schedule:** PAED: 2/4/2020 RTL: 10/3/2022 AWD: 3/21/2023 AC: 04/07/2023 CCA: 11/2025 EP: 12/2028

**Awarded Contractor:** Terracon Constructors Inc.

**EA 0Q690**

**Storm Damage; NAPA 12 PM 2.1/2.6 in County of Napa**

**Scope:** Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair

**Cost Estimate:** \$1.2M Construction Capital

**Schedule:** PAED:12/1/2020 RTL: 06/24/2022 AWD: 3/21/2023 AC: 03/03/2023 CCA: 10/30/2024 EP: 12/2026

---

<b>PIR</b> (Project Initiation Report)	<b>PSR</b> (Project Study Report)	<b>DED</b> (Draft Environmental Document)
<b>PAED</b> (Project Approval/ Environmental Document)		<b>PSE</b> (Plans, Specifications, and Estimate)
<b>RWC</b> (Right of Way Certification)	<b>RTL</b> (Ready to List)	<b>CCA</b> (Construction Contract Acceptance)
<b>ADV</b> (Advertise Contract)	<b>BO</b> (Bid Open)	<b>AWD</b> (Award Contract)

**EA 1G43A**

**Env. Mitigation at Conn Creek; NAPA 128 PM R7.4 on Silverado Trail in County of Napa**

**Scope:** Environmental mitigation, monitoring and report at Conn Creek

**Cost Estimate:** \$0.2M Construction Capital

**Schedule:** PAED: 10/5/2015 PS&E: 6/28/2021 RWC: 08/10/2021 RTL: 08/23/2021 AC: 07/26/2022 CCA: 10/2031

**EA 28120**

**Soscol Junction Improvement; NAPA 29 PM 5.0/7.1 and NAPA 221 PM 0.0/0.7 in County of Napa**

**Scope:** Construct New Interchange at SR 221/29/12

**Cost Estimate:** \$36.7M Construction Capital

**Schedule:** PAED: 2/13/2020 PSE: 08/26/2021 RWC: 08/25/2021 RTL: 08/26/21 AC: 05/13/2022 CCA: 11/2026

**EA 2Q260**

**Napa Valley Vine Trail; NAPA 29-PM 33.4/37.9 in County of Napa**

**Scope:** Construct Class 1 Multiuse Path

**Cost Estimate:** \$13.2M Construction Capital

**Schedule:** DED: 6/17/2020 PAED: 01/15/2021 PS&E: 12/10/2021 RWC: 12/10/2021 RTL: 12/10/2021

AWD: 5/20/2022 (Ghilotti Construction Company) AC: 06/15/2022 CCA: 02/27/2026

**EA 3G64A**

**Env. Mitigation & Plant Establishment at Napa River Bridge; NAPA 29 PM 37.0 in City of Calistoga**

**Scope:** Environmental mitigation at Napa River Bridge

**Cost Estimate:** \$0.5M Construction Capital

**Schedule:** PAED: 2/9/2015 RTL: 5/29/2019 AWD: 3/26/2020 (Hanford Applied) AC: 05/28/2020 CCA: 12/2028

**EA 4G210**

**Widen Roadway at Huichica Creek; NAPA 121-PM 0.75 in County of Napa**

**Scope:** Remove existing triple box culverts and replace with a new single span bridge

**Cost Estimate:** \$8.7M Construction Capital

**Schedule:** PAED: 4/9/2018 RTL: 12/8/2020 AWD: 5/19/2021 (Gordon Ball Inc) CCA: 04/30/2024 EP: 09/2026

**EA 4G21A**

**Env. Mitigation at Huichica Creek; NAPA 121-PM 0.75 in County of Napa**

**Scope:** Environmental mitigation, monitoring and report at Huichica Creek

**Cost Estimate:** \$1.0M Construction Capital

**Schedule:** PAED: 4/9/2018 RTL: 06/9/2023 AWD: 11/28/2023 AC: 12/20/2023 CCA: 06/2033

**EA 4G84A**

**Capell Creek Bridge Env Mitigation; NAPA 128-PM 20.2 in County of Napa**

**Scope:** Environmental Permit Mitigation & Plant Establishment to Bridge Replacement

**Cost Estimate:** \$0.5M Construction Capital

**Schedule:** PAED: 6/16/2016 RTL: 05/23/2022 AWD: 11/17/2022 CCA: 11/2031

**ACTION ITEMS**

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)


**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)



# Caltrans District 4 Active Projects in Napa County

April 2026

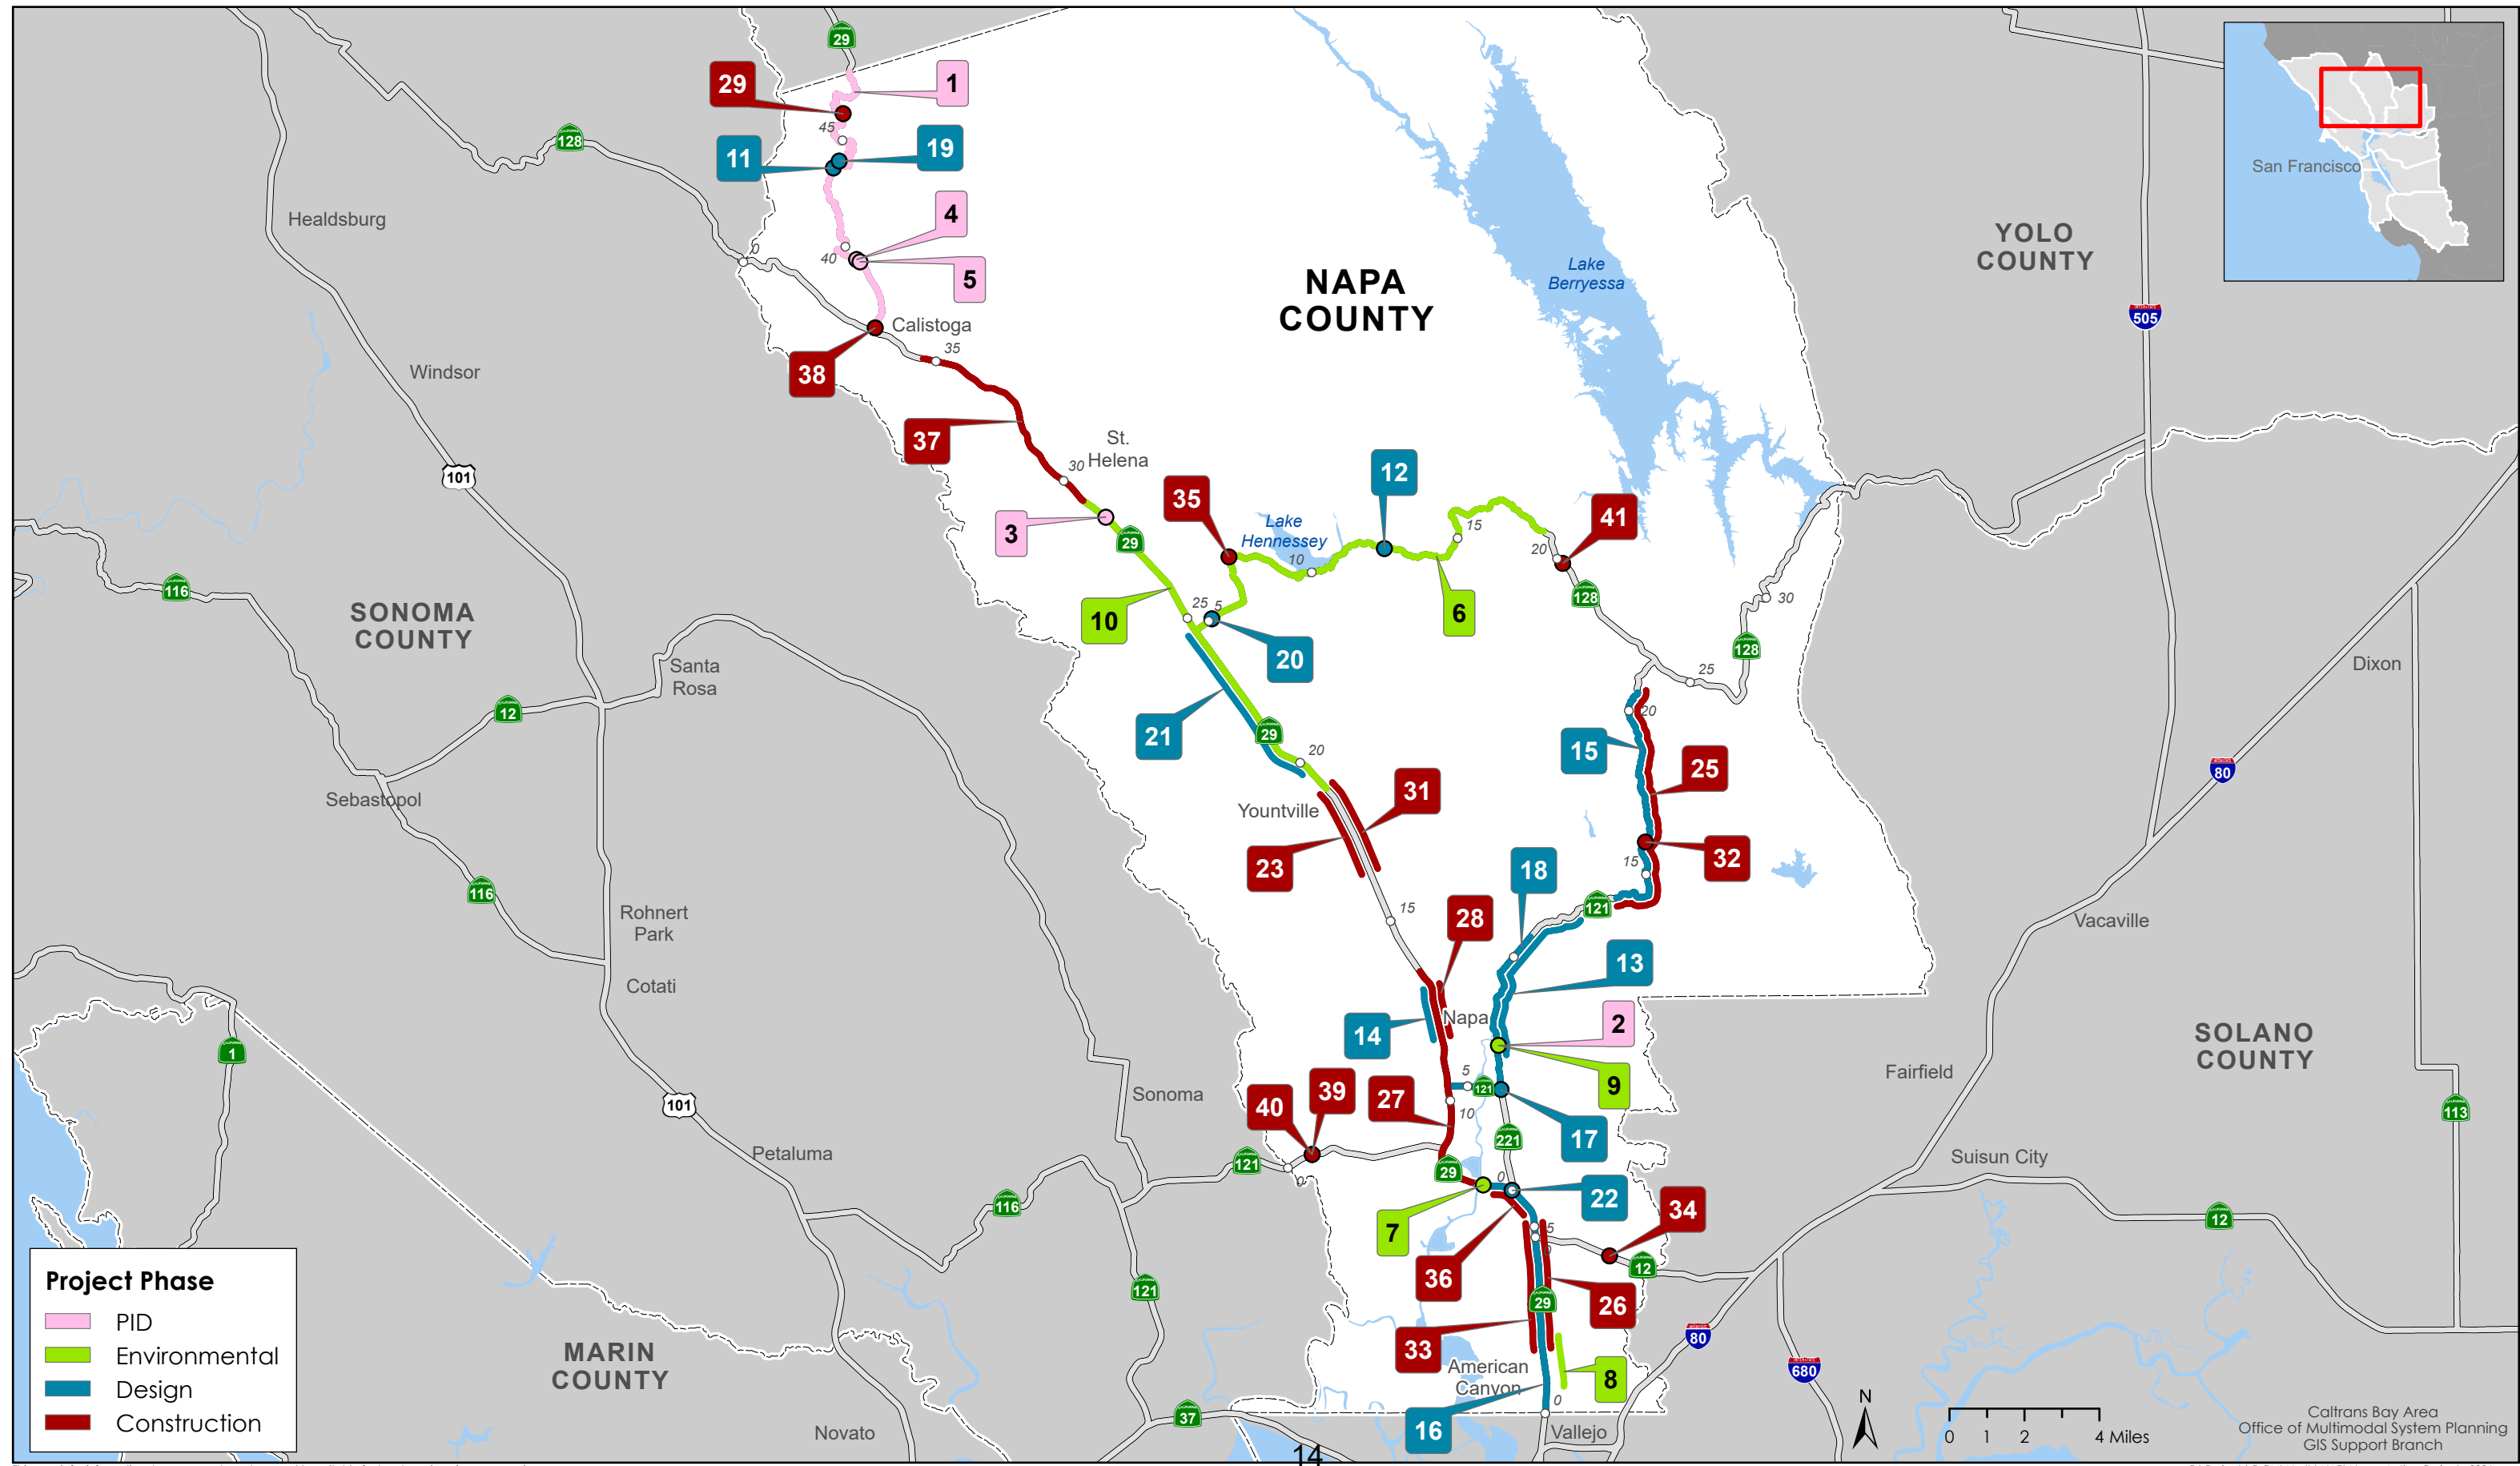

This map is for informational purposes only and may not be suitable for legal, engineering, or surveying purposes.

**Caltrans District 4 Active Projects in Napa County - April 2026**

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
1	PID	2Q510	29	36.8/48.6	Pavement rehabilitation	TBD	TBD	05/2030	12/2030	05/2031
2	PID	4Y400	121	7.2/7.2	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
3	PID	0W750	29	28.485/28.485	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
4	PID	1X750	29	39.08	Garnett Creek Bridge Replacement	TBD	TBD	TBD	TBD	TBD
5	PID	1X760	29	38.96	Garnett Creek Branch Bridge Replacement	\$18.1M	10/2029	10/2032	04/2033	12/2034
6	Environmental	2W880	128	4.56/19.1	Napa City Pavement Preservation	\$13.8M	10/2026	05/2028	03/2029	11/2038
7	Environmental	4W370	29	6.99/6.99	Bridge Scour Mitigation	\$14.6M	10/2027	07/2029	01/2030	01/2031
8	Environmental	4Q010	29	0.69/R2.054	Multi-Modal Corridor Improvements	\$53.1M	07/2026	06/2028	01/2029	06/2030
9	Environmental	0J890	121	7.20/7.40	Intersection Improvement	\$18.0 M ( \$1.0M SHOPP Contribution)	5/1/2026	4/30/2028	12/1/2028	12/2030
10	Environmental	0X110	29	19.00/29.25	Napa Valley Vine Trail gap closure project	\$25.3M	05/2026	11/2027	05/2028	07/2029
11	Design	2W370	29	42.57	Replace failed netting with new netting, remove debris, and install additional erosion control.	\$1.8M	4/28/2025	03/2026	02/2027	05/2028
12	Design	4AA30	128	12.5	Storm Damage Restoration	\$5.3M	12/18/2024	10/2026	05/2027	06/2028
13	Design	0Q800	121	6.9/12.1	Permanent Restoration; Inject grout at sinkhole and install drainage	\$997K	10/15/2024	03/2026	12/2026	12/2027
14	Design	0Q82A	29	11.6/13	Lincoln Ave Mitigation & Bio Monitoring	\$253K	N/A	05/2026	10/2026	09/2030
15	Design	0Q79A	121	13.4/20.7	Env Mitigation for 0Q790	\$600K	N/A	06/2027	12/2027	12/2036
16	Design	4AC80	29	0.0/7.0	Pavement rehabilitation	\$18.9M	6/28/2024	11/2026	06/2027	01/2028
17	Design	4J820	121	5.9	Bridge Replacement	\$15.6M	3/27/2023	08/2028	02/2029	12/2030
18	Design	1Q620	121	4.47/10.7	Pavement repair	\$35M	6/30/2022	08/2027	03/2028	06/2029
19	Design	2J88U	29	42.83	Sub-structure rehabilitation and-One Bridge scour mitigation	\$2.2M	2/1/2019	10/13/2025	12/2026	12/2028
20	Design	4J830	128	5.1	Bridge Replacement	\$12.2M	6/29/2022	08/2027	02/2028	12/2030
21	Design	2W430	29	19.70/24.60	Operational and Safety Improvements	\$8.55M	5/16/2025	07/2026	09/2026	08/2028
22	Design	4W940	221	0	Devlin/ Soscol Ferry Roundabout	\$4.057M	12/17/2021	01/2026	05/2026	10/2027
23	Construction	0K63A	29	16.5/19.00	Plant Establishment and Environmental Mitigation	\$265K	N/A	4/21/2025	10/2025	06/2028
24(Not mapped)	Construction	4AC90	VAR	Var	Install/ Upgrade Horizontal Alignment Warning Signs	\$5.56M	6/21/2024	06/2025	12/2025	04/2028
25	Construction	0Q790	121	13.37/20.73	Construct RSP at five slipout locations.	\$6.4M	2/9/2023	5/5/2025	11/2025	12/2027
26	Construction	4J411	29	1.7/5.1	Sheehy Xrk Plant Mitigation	\$596K	N/A	4/9/2025	11/26/2025	12/2035
27	Construction	2Q610	29	R7.3/13.5	Pavement rehabilitation.	\$23.3M	4/20/2022	5/3/2024	11/27/2024	11/2026
28	Construction	0Q820	29	11.6/13.0	Repair Culvert and stabilize the roadway.	\$24.47M	9/10/2021	12/4/2023	10/1/2024	12/2026
29	Construction	0Q830	29	46.1	Construct CIDH segmented pile wall at slipout	\$1.7M	6/29/2022	1/22/2024	7/12/2024	03/2026
30(Not mapped)	Construction	3Q760	29	Var	Construct rumble strips at seven locations.	\$3.3M	12/31/2021	6/26/2023	3/27/2024	12/31/2024
31	Construction	0K630	29	16.48/19.04	Upgrade / Replace Bridge Rails	\$4.7M	10/22/2020	12/5/2022	7/14/2023	11/2025
32	Construction	0Q810	121	16.0/16.1	Repair pavement, replace drainage systems and upgrade guardrail.	\$1.3M	2/2/2022	6/26/2023	1/23/2024	12/2/2024
33	Construction	4J410	29	1.7/5.1	Rehabilitate Culverts	\$3.3M	2/4/2020	10/3/2022	4/7/2023	11/2025
34	Construction	0Q690	12	2.1/2.6	Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair	\$1.2M	12/1/2020	6/24/2022	3/3/2023	10/30/2024
35	Construction	1G43A	128	R7.4	Environmental mitigation, monitoring and report at Conn Creek	\$0.2M	10/5/2015	8/23/2021	7/26/2022	10/2031
36	Construction	28120	29	5.45/R6.7	Construct New Interchange at SR 221/29/12	\$36.7M	2/13/2020	8/26/2021	5/13/2022	11/2026
37	Construction	2Q260	29	29.24/35.34	Construct Class 1 Multiuse Path	13.2M	11/6/2020	12/10/2021	6/15/2022	10/2025
38	Construction	3G64A	29	37.0	Environmental mitigation at Napa River Bridge	\$0.5M	2/9/2015	5/29/2019	5/28/2020	12/2028

**Caltrans District 4 Active Projects in Napa County - April 2026**

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
<b>39</b>	Construction	4G210	121	0.75	Remove existing triple box culverts and replace with a new single span bridge	\$8.7M	4/9/2018	12/8/2020	6/10/2021	4/30/2024
<b>40</b>	Construction	4G21A	121	0.75	Environmental mitigation, monitoring and report at Huichica Creek	\$1M	4/9/2018	6/9/2023	12/20/2023	6/30/2033
<b>41</b>	Construction	4G84A	128	20.2	Environmental Permit Mitigation & Plant Establishment to Bridge Replacement	\$0.5M	6/16/2016	5/23/2022	12/21/2022	11/17/2031
