



---

## NAPA VALLEY TRANSPORTATION AUTHORITY Staff Report

---

**TO:** Technical Advisory Committee  
**FROM:** Danielle Schmitz, Executive Director  
**REPORT BY:** Jonathan Stanton, Associate Planner  
(707) 259-8634 / Email: [jstanton@nvta.ca.gov](mailto:jstanton@nvta.ca.gov)  
**SUBJECT:** Caltrans SHOPP Projects Update

---

### **RECOMMENDATION**

Information only

### **EXECUTIVE SUMMARY**

California Transportation Commission (CTC) recently adopted the 2026 State Highway Operations and Protection Program (SHOPP), which funds the repair and preservation, emergency repairs, safety improvements, and some highway operational improvements on state highways. The adopted program includes \$17.8 billion in funding over Fiscal Years (FY) 2026-27 through 2029-30, and almost 600 projects.

There are 12 Napa County 2026 SHOPP projects in total representing \$334,908,000 in investment. Two new projects in Napa County were nominated and added to the 2026 SHOPP, both the new projects are on SR 29 north of Calistoga. Ten additional Napa County projects in the 2026 SHOPP are carried over from the previous SHOPP. Projects in the Project Initiation Document (PID) phase present the best opportunity for local jurisdictions to work with Caltrans and NVRTA to adjust and modify project scope, limits, and key elements.

### **FINANCIAL IMPACT**

None/information only.

### **BACKGROUND AND DISCUSSION**

Recap: The 2026 SHOPP was approved by CTC during the March 2026 meeting. The 2026 SHOPP includes over \$17 billion in programmed and reserved funding over its 4-year planning horizon.

Funding for the 2026 SHOPP program cycle has been reduced by approximately \$1 billion per year, compared to previous years. Funding reductions are a result of recent program oversubscription associated emergency work on the State Highway System, particularly repairs related to early pavement degradation and storm damage. Recent work on State Route 29 between Madison Ave. and Yount Mill Rd. to fix pavement rutting and a culvert replacement between Oakville Cross Rd. and Rutherford Rd/SR 128 are examples of emergency repair work funded through the SHOPP program.

The 2026 SHOPP portfolio includes 593 projects, of which 498 are carryover projects and 95 new. By contrast, the 2024 SHOPP portfolio included 427 carryover projects and 208 new projects. 12 SHOPP projects are in Napa County, including 10 carryover projects and two new projects, totaling \$334,908,000.

Two Napa County projects currently in the Project Initiation Document (PID) phase were nominated and added to 2026 SHOPP as new long lead projects. Long Lead projects are projects which require more than four years to develop due to complex environmental and preliminary engineering work. Programming Long Lead projects into SHOPP allows Caltrans to begin work on the Project Approval and Environmental Document (PA&ED) phase:

**2Q510** – Pavement Rehabilitation on SR 29 from the Lake County line to approximately 6.5 miles south (postmile 42.1 to 48.6).

**1X760** – Garnett Creek Branch Bridge Replacement, located on SR 29 north of the City of Calistoga, Postmile 38.96.

Additional project information can be found in the active projects table and map in Attachment 1.

With successful nomination, these two projects will now proceed to the next phase of Caltrans project development, PA&ED, where Caltrans will further develop the projects to obtain environmental clearance before moving to the design (PS&E) phase. Detailed information about these projects can be found in attachment A, Caltrans Active Projects list.

Other Napa projects in the PID phase were either not nominated or not selected to be included in the 2026 SHOPP program. All other Napa County projects in the SHOPP program are carryovers from 2024 SHOPP, examples of carryover projects include:

**4AC80** – repaving SR 29 between Solano County line and Napa River Bridge, and

**4J820** – Tulucay Creek bridge replacement in the City of Napa.

---

Projects in the PID phase present the best opportunity to work with Caltrans to adjust and modify project goals, details, and extents. Generally, construction can be expected to start around 5 years from completion of PID phase. Early coordination with Caltrans is advised to align project scope and key elements with local priorities. Jurisdictions can work with NVTa to identify projects in early phases and assist in coordination through monthly meetings held between Caltrans and NVTa or facilitated discussions with Napa County Caltrans liaisons and functional unit staff.

NVTa and Caltrans District 4 also support nominating non-SHOPP projects to PID phase. Caltrans Planning released State-Sponsored Non-SHOPP PID Nomination intake in February of this year. NVTa nominated 7 projects, and one project was selected by District 4 staff to advance to Caltrans Headquarters for consideration: SR 121/221/ Imola Ave. Intersection Safety and Operational Improvements. If selected, Caltrans, in coordination with NVTa, will develop multimodal improvements at the intersection including connections to Magnolia Way. Selection of nominated projects is expected to be announced in June 2026.

### **ATTACHMENT**

1. Caltrans Active Projects List & Map, May 2026.

**PROJECT INITIATION REPORT**

**EA 4Y400**

**Operational Improvement; NAPA 121 PM 7.2 at Hennessy Drive in the City of Napa**

Scope: Operational Improvement

**EA 2Q510 - Nominated in 2026 SHOPP**

**Pavement Rehab; NAPA 29 PM 42.1/48.6 in County of Napa**

Scope: Pavement rehabilitation and Safety Improvements

**EA 0W750**

**Intersection Improvement; NAPA 29 PM 28.485 at Pope St. in the City of St. Helena**

Scope: Intersection Improvement

**EA 1X750**

**Garnett Creek Bridge Replacement; NAPA 29 PM 39.08 in the City of Calistoga**

Scope: Bridge Replacement

**EA 1X760 - Nominated in 2026 SHOPP**

**Garnett Creek Branch Bridge Replacement; NAPA 29 PM 38.96 near the City of Calistoga**

Scope: Bridge Replacement

Target Delivery Year: FY 2032/2033

**ENVIRONMENTAL**

**EA 2W880**

**Pavement Preservation; NAP 128 PM 4.56/19.10 in County of Napa from R29 to Knoxville Road**

Scope: Pavement Preservation

Cost Estimate: \$27 M Construction Capital

Schedule: **PAED: 04/2027**      **PS&E: 11/2028**      **RWC: 12/2028**      **RTL: 01/2029**

**EA 4W370**

**Bridge Scour Mitigation; NAPA 29 PM 6.99 in County of Napa at the Napa River BOH (aka George Butler Bridge)**

Scope: Scour Mitigation and Seismic Retrofit.

Cost Estimate: \$14.6 M Construction Capital

Schedule: **PAED: 10/2027**      **PS&E: 4/2029**      **RWC: 5/2029**      **RTL: 7/2029**

**EA 4Q010**

**NAPA 29 PM 0.6/R2.5 in City of American Canyon**

Scope: Multi-Modal Corridor Improvements

Between Napa Junction Rd and American Canyon Rd

Cost Estimate: \$ 53.1 M Construction Capital

Schedule: **PSR/PDS: 2/6/2023**      **PAED: 12/2026**      **PS&E: 12/2027**      **RWC: 6/2028**      **RTL: 6/2028**

A PAED coop agreement is executed on 2/29/2024

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0J890**

**5-Way Intersection; NAPA 121-PM 7.3 in City of Napa**

**Scope:** Intersection Improvement

At the intersection of Rt 121, Third St, East Ave and Coombsville

**Cost Estimate:** \$34.95 M Construction Capital (\$3.90 M SHOPP Contribution)

**Schedule:** DED: 08/28/2025      **PAED: 8/2026**      PS&E: 4/2028      RWC: 4/202      **RTL: 4/2028**

A coop agreement is executed on 8/28/2023

**EA 0X110**

**Napa Valley Vine Trail Gap Closure; NAPA 29 PM 19.00/29.25 in County of Napa**

**Scope:** Construct Class I & Class III Bicycle Facilities

From California Drive in the Town of Yountville to Pratt Ave

**Cost Estimate:** \$25.3 M Construction Capital

**Schedule:** DED: 09/2026      **PAED: 12/2026**      PS&E: 2/202      RWC: 9/2027      **RTL: 11/2028**

**DESIGN**

**EA 2W370**

**Major Damage; NAPA 29 PM 42.57 in County of Napa**

**Scope:** Replace failed netting with new netting, remove debris, and install additional erosion control.

**Cost Estimate:** \$1.8 M Construction Capital

**Schedule:** PAED: 4/28/2025      **PS&E: 4/3/2026**      **RWC: 4/6/2026**      **RTL: 4/14/2026**

**EA 4AA30**

**Storm Damage; NAPA 128 PM 12.5 in County of Napa**

**Scope:** Storm Damage Restoration – Install Soil Nail Wall

**Cost Estimate:** \$5.3 M Construction Capital

**Schedule:** PAED: 12/18/2024      PS&E: 08/2026      **RWC: 10/2026**      **RTL: 11/2026**

**EA 0Q800**

**Major Damage; NAPA 121 PM 6.9/12.1 in County of Napa**

**Scope:** Permanent Restoration; Inject grout at sinkhole and install drainage

**Cost Estimate:** 1 M Construction Capital

**Schedule:** PA&ED: 10/15/2024      **PS&E: 03/27/2026**      **RWC: 03/30/2026**      **RTL: 03/30/2026**

**EA 0Q82A**

**Mitigation & Bio Monitoring for Storm Damage; NAPA 29 PM 11.6/13.0 in County of Napa**

**Scope:** Environmental mitigation at Multiple Locations

**Cost Estimate:** 253K Construction Capital

**Schedule:** PS&E: 3/04/2026      RWC: 3/13/2026      **RTL: 4/10/2026**

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0Q79A**

**Mitigation & Bio Monitoring for Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$600 K Construction Capital

Schedule: PS&E: 4/2027 RWC: 6/2027 RTL: 6/2027

**EA 4AC80**

**Pavement Rehab; NAPA 29 PM 0.0/7.0 in American Canyon & County of Napa**

Scope: Pavement rehabilitation

Cost Estimate: \$18.91 M Construction Capital

Schedule: PAED: 6/28/2024 PS&E: 9/2026 RWC:10/2026 RTL: 11/2026

**EA 4J820**

**Tulucay Creek Bridge Replacement; NAPA 121 PM 5.9 in City of Napa**

Scope: Bridge Replacement

Cost Estimate: \$15.6M Construction Capital

Schedule: DED: 06/30/2022 PAED: 03/27/2023 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

**EA 1Q620**

**Pavement Rehab; NAPA 121 PM 4.47/10.7 in City of Napa**

Scope: Pavement repair.

Cost Estimate: \$39.6 M Construction Capital

Schedule: PAED: 06/30/2022 PS&E: 06/2027 RWC: 08/2027 RTL: 08/2027

**EA 2J88U**

**No-Name Creek Bridge: NAPA 29-PM 42.83 in County of Napa**

Scope: Sub-structure rehabilitation and scour mitigation at one bridge

Cost Estimate: \$2.20M Construction Capital

Schedule: PAED: 2/1/2019 PS&E: 10/09/2025 RWC: 10//09/2025 RTL: 10/13/2025 AWD: 11/2026 AC: 12/2026

**EA 4J830**

**Hopper Slough Creek; NAPA 128 PM 5.1 in County of Napa**

Scope: Bridge Replacement

Cost Estimate: 12.2 M Construction Capital

Schedule: DED: 03/18/2022 PAED: 06/29/2022 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

**EA 2W430**

**Napa Forward Intersection Improvements; NAPA 29 PM 22.72 in County of Napa**

Scope: Operational and Safety Improvements at the intersection of Oakville Cross Rd and Rutherford Rd

Cost Estimate: \$8.5 M Construction Capital

Schedule: DED: 01/31/2024 PAED: 05/16/2025 PS&E: 06/2026 RWC: 07/2026 RTL: 07/2026

---

<b>PIR</b> (Project Initiation Report)	<b>PSR</b> (Project Study Report)	<b>DED</b> (Draft Environmental Document)
<b>PAED</b> (Project Approval/ Environmental Document)		<b>PSE</b> (Plans, Specifications, and Estimate)
<b>RWC</b> (Right of Way Certification)	<b>RTL</b> (Ready to List)	<b>CCA</b> (Construction Contract Acceptance)
<b>ADV</b> (Advertise Contract)	<b>BO</b> (Bid Open)	<b>AWD</b> (Award Contract)

**EA 4W940**

**Devlin/ Soscol Ferry Roundabout; NAPA 221-PM 0.00 in County of Napa**

**Scope:** Construct Roundabout (DEER – Oversight by Napa County)

**Cost Estimate:** \$4.057M Construction Capital

**Schedule:** PS&E: 07/16/2025 RWC: N/A RTL: Pending Napa County Submission of Encroachment Permit

**CONSTRUCTION**

**EA 0K63A**

**Plant Establishment and Environmental Mitigation; NAPA 29 PM 1.7/PM 5.1 in County of Napa**

**Scope:** Plant establishment and environmental mitigation and monitoring work for bridge rail upgrade EA 0K630 In and near Yountville, at Dry Creek Bridge, Perfume Creek Bridge and California Drive UC.

**Cost Estimate:** \$0.31 M Construction Capital

**Schedule:** PS&E: 03/18/2025 RWC: 04/02/2025 RTL: 04/21/2025 AC: 02/27/2026 CCA: 6/2028

**EA 4AC90**

**Safety; Various Locations in County of Napa**

**Scope:** Install/ Upgrade Horizontal Alignment Warning Signs

**Cost Estimate:** \$4.47 M Construction Capital

**Schedule:** PAED: 6/21/2024 PS&E: 6/20/2025 RWC: 6/20/2025 RTL: 6/25/2025 AC: 12/30/2025 CCA: 12/2026

**EA 0Q790**

**Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

**Scope:** Construct RSP at five slip-out locations.

**Cost Estimate:** \$2.4 M Construction Capital

**Schedule:** PAED: 02/9/2023 PS&E: 04/16/2025 RWC: 04/24/2025 RTL: 05/05/2025 AC: 11/18/2025 CCA: 12/2027

**EA 4J411**

**Mitigation and Bio monitoring; NAPA 29 PM 1.7/PM 5.1 in American Canyon**

**Scope:** Plant establishment and monitoring work for drainage improvement EA 4J410 at Rio Del Mar

**Cost Estimate:** \$0.60 M Construction Capital

**Schedule:** PS&E: 02/4/2025 RWC: 02/11/2025 RTL: 04/9/2025 AC: 11/26/2025 CCA: 12/2035

**EA 2Q610**

**Pavement Rehab; NAPA 29 PM R7.3/13.5 in County of Napa**

**Scope:** Pavement rehabilitation.

**Cost Estimate:** \$23.3M Construction Capital

**Schedule:** PAED: 04/20/2022 PS&E: 04/23/2024 RWC: 04/24/2024 RTL: 05/03/2024 AC: 11/26/2024 CCA: 10/2026

**Awarded Contractor:** Granite Rock Company

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)

**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)

**EA 0Q820**

**Storm Damage; NAPA 29 PM 11.6/13.0 in City of Napa**

**Scope:** Repair Culvert and stabilize the roadway at Lincoln Ave

**Cost Estimate:** \$24.475M Construction Capital

**Schedule:** PAED: 09/10/2021 PS&E: 11/2023 RWC: 11/2023 RTL: 12/2023 AC: 10/2024 CCA: 12/2027

**EA 0Q830**

**Storm Damage; NAPA 29 PM 46.1 in County of Napa**

**Scope:** Construct CIDH segmented pile wall at slip out

**Cost Estimate:** \$1.7M Construction Capital

**Schedule:** PAED: 06/29/2022 RWC:1/11/2024 RTL: 1/22/2024 AC: 07/12/2024 CCA: 03/20/2026 EP: 9/2027

**EA 3Q760**

**Rumble Strips; NAPA 29, 121 & 128 Various Locations in County of Napa**

**Scope:** Construct rumble strips at seven locations.

**Cost Estimate:** \$3.3M Construction Capital

**Schedule:** PAED: 12/31/2021 RTL: 6/26/2023 AWD: 2/29/2024 AC: 03/27/2024 CCA 12/31/2024 EP: 12/2026

**EA 0K630**

**Bridge Rails; NAPA 29 PM 16.48/19.04 in County of Napa**

**Scope:** Upgrade / Replace Bridge Rails in 3 Bridges

**Cost Estimate:** \$4.7M Construction Capital

**Schedule:** PAED:10/22/2020 RWC:12/05/2022 RTL:12/05/2022 AC: 07/14/2023 CCA: 02/02/2026 EP: 04/2027

**EA 0Q810**

**Storm Damage; NAPA 121 PM 16.0/16.1 in County of Napa**

**Scope:** Repair pavement, replace drainage systems and upgrade guardrail.

**Cost Estimate:** \$1.3M Construction Capital

**Schedule:** PAED: 02/02/2022 RTL: 06/26/2023 AWD: 12/29/2023 AC: 1/23/2024 CCA:12/2/2024 EP: 05/2026

**Awarded Contractor:** Argonaut Constructors

**EA 4J410**

**Drainage Improvement; NAPA 29 PM 1.7/5.1 in City of American Canyon**

**Scope:** Rehabilitate Culverts

**Cost Estimate:** \$3.3M Construction Capital

**Schedule:** PAED: 2/4/2020 RTL: 10/3/2022 AWD: 3/21/2023 AC: 04/07/2023 CCA: 11/2025 EP: 12/2028

**Awarded Contractor:** Terracon Constructors Inc.

**EA 0Q690**

**Storm Damage; NAPA 12 PM 2.1/2.6 in County of Napa**

**Scope:** Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair

**Cost Estimate:** \$1.2M Construction Capital

**Schedule:** PAED:12/1/2020 RTL: 06/24/2022 AWD: 3/21/2023 AC: 03/03/2023 CCA: 10/30/2024 EP: 12/2026

---

<b>PIR</b> (Project Initiation Report)	<b>PSR</b> (Project Study Report)	<b>DED</b> (Draft Environmental Document)
<b>PAED</b> (Project Approval/ Environmental Document)		<b>PSE</b> (Plans, Specifications, and Estimate)
<b>RWC</b> (Right of Way Certification)	<b>RTL</b> (Ready to List)	<b>CCA</b> (Construction Contract Acceptance)
<b>ADV</b> (Advertise Contract)	<b>BO</b> (Bid Open)	<b>AWD</b> (Award Contract)

**EA 1G43A**

**Env. Mitigation at Conn Creek; NAPA 128 PM R7.4 on Silverado Trail in County of Napa**

**Scope:** Environmental mitigation, monitoring and report at Conn Creek

**Cost Estimate:** \$0.2M Construction Capital

**Schedule:** PAED: 10/5/2015 PS&E: 6/28/2021 RWC: 08/10/2021 RTL: 08/23/2021 AC: 07/26/2022 CCA: 10/2031

**EA 28120**

**Soscol Junction Improvement; NAPA 29 PM 5.0/7.1 and NAPA 221 PM 0.0/0.7 in County of Napa**

**Scope:** Construct New Interchange at SR 221/29/12

**Cost Estimate:** \$36.7M Construction Capital

**Schedule:** PAED: 2/13/2020 PSE: 08/26/2021 RWC: 08/25/2021 RTL: 08/26/21 AC: 05/13/2022 CCA: 11/2026

**EA 2Q260**

**Napa Valley Vine Trail; NAPA 29-PM 33.4/37.9 in County of Napa**

**Scope:** Construct Class 1 Multiuse Path

**Cost Estimate:** \$13.2M Construction Capital

**Schedule:** DED: 6/17/2020 PAED: 01/15/2021 PS&E: 12/10/2021 RWC: 12/10/2021 RTL: 12/10/2021

AWD: 5/20/2022 (Ghilotti Construction Company) AC: 06/15/2022 CCA: 02/27/2026

**EA 3G64A**

**Env. Mitigation & Plant Establishment at Napa River Bridge; NAPA 29 PM 37.0 in City of Calistoga**

**Scope:** Environmental mitigation at Napa River Bridge

**Cost Estimate:** \$0.5M Construction Capital

**Schedule:** PAED: 2/9/2015 RTL: 5/29/2019 AWD: 3/26/2020 (Hanford Applied) AC: 05/28/2020 CCA: 12/2028

**EA 4G210**

**Widen Roadway at Huichica Creek; NAPA 121-PM 0.75 in County of Napa**

**Scope:** Remove existing triple box culverts and replace with a new single span bridge

**Cost Estimate:** \$8.7M Construction Capital

**Schedule:** PAED: 4/9/2018 RTL: 12/8/2020 AWD: 5/19/2021 (Gordon Ball Inc) CCA: 04/30/2024 EP: 09/2026

**EA 4G21A**

**Env. Mitigation at Huichica Creek; NAPA 121-PM 0.75 in County of Napa**

**Scope:** Environmental mitigation, monitoring and report at Huichica Creek

**Cost Estimate:** \$1.0M Construction Capital

**Schedule:** PAED: 4/9/2018 RTL: 06/9/2023 AWD: 11/28/2023 AC: 12/20/2023 CCA: 06/2033

**EA 4G84A**

**Capell Creek Bridge Env Mitigation; NAPA 128-PM 20.2 in County of Napa**

**Scope:** Environmental Permit Mitigation & Plant Establishment to Bridge Replacement

**Cost Estimate:** \$0.5M Construction Capital

**Schedule:** PAED: 6/16/2016 RTL: 05/23/2022 AWD: 11/17/2022 CCA: 11/2031

**ACTION ITEMS**

**PIR** (Project Initiation Report)

**PAED** (Project Approval/ Environmental Document)

**RWC** (Right of Way Certification)

**ADV** (Advertise Contract)

**PSR** (Project Study Report)

**RTL** (Ready to List)

**BO** (Bid Open)

**DED** (Draft Environmental Document)

**PSE** (Plans, Specifications, and Estimate)


**CCA** (Construction Contract Acceptance)

**AWD** (Award Contract)




# Caltrans District 4 Active Projects in Napa County

May 2026

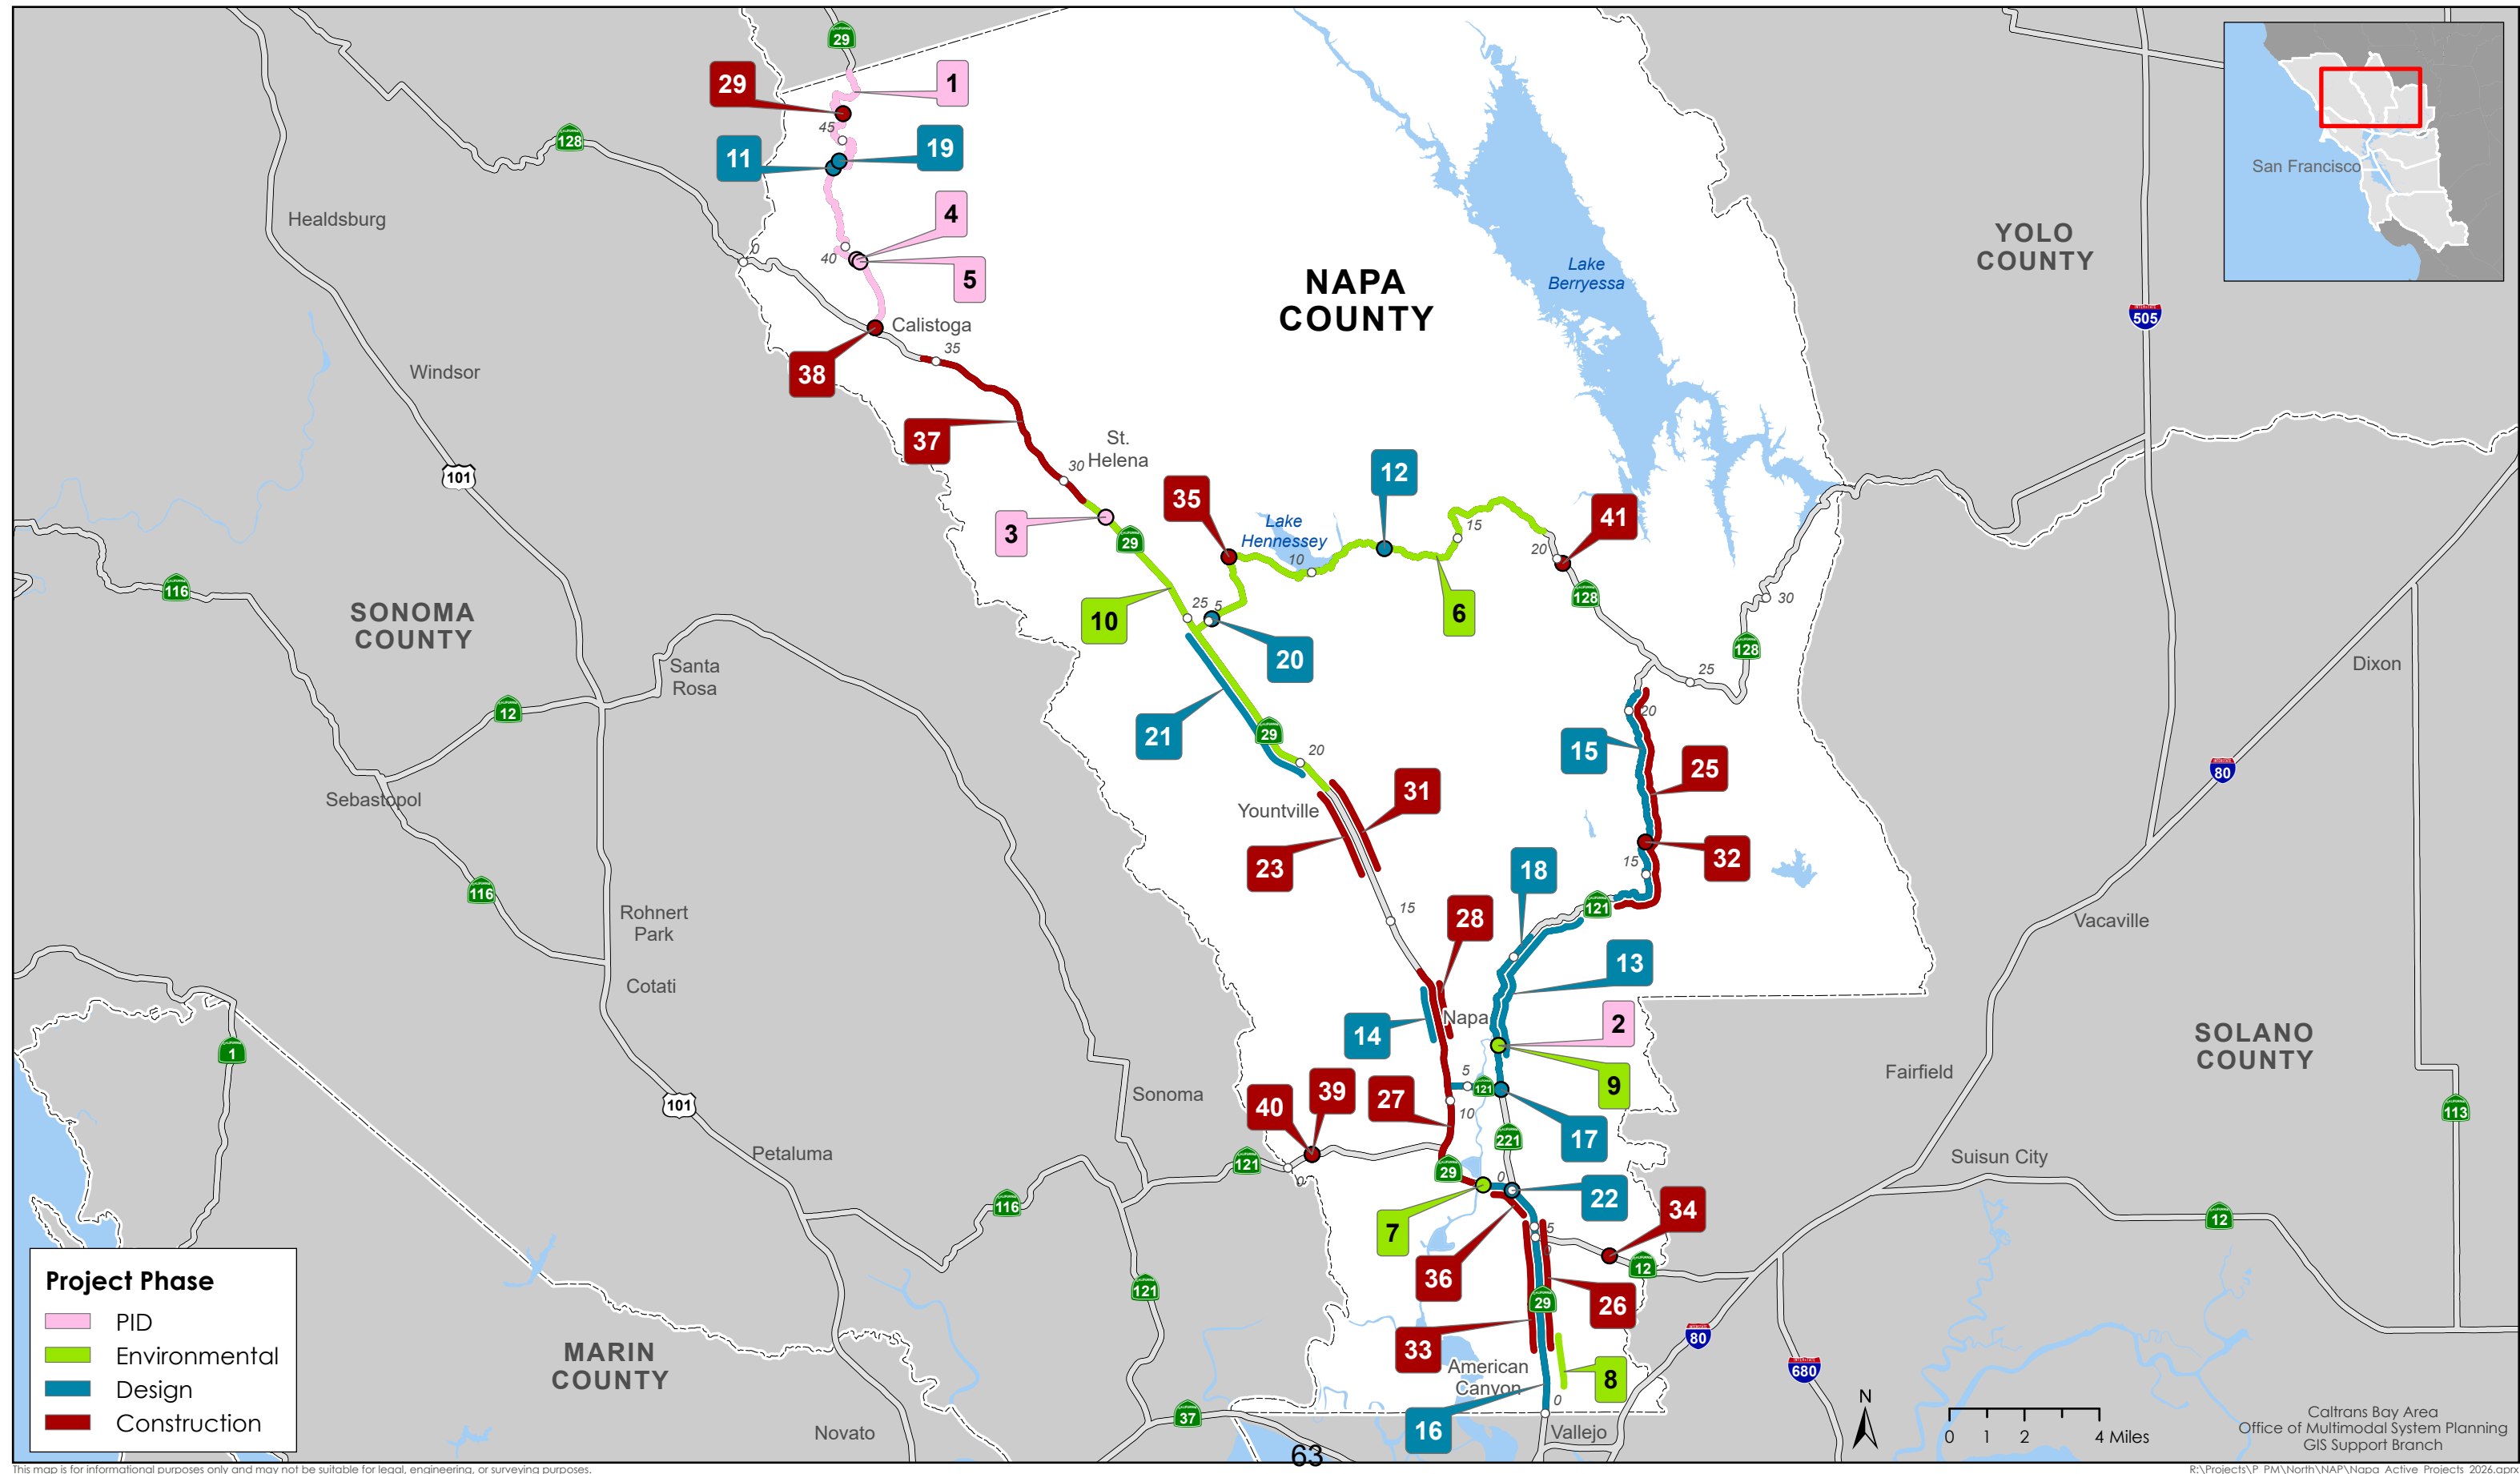

**Project Phase**

- PID
- Environmental
- Design
- Construction



Caltrans Bay Area  
Office of Multimodal System Planning  
GIS Support Branch

This map is for informational purposes only and may not be suitable for legal, engineering, or surveying purposes.

R:\Projects\VP\_PM\North\NAPA\Napa\_Active\_Projects\_2026.aprx

**Caltrans District 4 Active Projects in Napa County - May 2026**

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
1	PID	2Q510	29	36.8/48.6	Pavement rehabilitation	TBD	TBD	05/2030	12/2030	05/2031
2	PID	4Y400	121	7.2/7.2	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
3	PID	0W750	29	28.485/28.485	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
4	PID	1X750	29	39.08	Garnett Creek Bridge Replacement	TBD	TBD	TBD	TBD	TBD
5	PID	1X760	29	38.96	Garnett Creek Branch Bridge Replacement	\$18.1M	10/2029	10/2032	04/2033	12/2034
6	Environmental	2W880	128	4.56/19.1	Napa City Pavement Preservation	\$27.0M	04/2027	01/2029	07/2029	11/2031
7	Environmental	4W370	29	6.99/6.99	Bridge Scour Mitigation	\$14.6M	10/2027	07/2029	01/2030	01/2031
8	Environmental	4Q010	29	0.69/R2.054	Multi-Modal Corridor Improvements	\$53.1M	07/2026	06/2028	01/2029	06/2030
9	Environmental	0J890	121	7.20/7.40	Intersection Improvement	\$18.0 M ( \$1.0M SHOPP Contribution)	8/1/2026	4/30/2028	12/1/2028	12/2030
10	Environmental	0X110	29	19.00/29.25	Napa Valley Vine Trail gap closure project	\$25.3M	05/2026	11/2028	05/2028	07/2029
11	Design	2W370	29	42.57	Replace failed netting with new netting, remove debris, and install additional erosion control.	\$1.8M	4/28/2025	04/14/2026	02/2027	05/2028
12	Design	4AA30	128	12.5	Storm Damage Restoration	\$5.3M	12/18/2024	11/2026	05/2027	06/2028
13	Design	0Q800	121	6.9/12.1	Permanent Restoration; Inject grout at sinkhole and install drainage	\$997K	10/15/2024	03/30/2026	12/2026	12/2027
14	Design	0Q82A	29	11.6/13	Lincoln Ave Mitigation & Bio Monitoring	\$253K	N/A	04/10/2026	10/2026	09/2030
15	Design	0Q79A	121	13.4/20.7	Env Mitigation for 0Q790	\$600K	N/A	06/2027	12/2027	12/2036
16	Design	4AC80	29	0.0/7.0	Pavement rehabilitation	\$18.9M	6/28/2024	11/2026	06/2027	01/2028
17	Design	4J820	121	5.9	Bridge Replacement	\$15.6M	3/27/2023	08/2028	02/2029	12/2030
18	Design	1Q620	121	4.47/10.7	Pavement repair	\$35M	6/30/2022	08/2027	03/2028	06/2029
19	Design	2J88U	29	42.83	Sub-structure rehabilitation and-One Bridge scour mitigation	\$2.2M	2/1/2019	10/13/2025	12/2026	12/2028
20	Design	4J830	128	5.1	Bridge Replacement	\$12.2M	6/29/2022	08/2027	02/2028	12/2030
21	Design	2W430	29	19.70/24.60	Operational and Safety Improvements	\$8.55M	5/16/2025	07/2026	09/2026	08/2028
22	Design	4W940	221	0	Devlin/ Soscol Ferry Roundabout	\$4.057M	12/17/2021	01/2026	05/2026	10/2027
23	Construction	0K63A	29	16.5/19.00	Plant Establishment and Environmental Mitigation	\$265K	N/A	4/21/2025	10/2025	06/2028
24(Not mapped)	Construction	4AC90	VAR	Var	Install/ Upgrade Horizontal Alignment Warning Signs	\$5.56M	6/21/2024	06/2025	12/2025	04/2028
25	Construction	0Q790	121	13.37/20.73	Construct RSP at five slipout locations.	\$6.4M	2/9/2023	5/5/2025	11/2025	12/2027
26	Construction	4J411	29	1.7/5.1	Sheehy Xrk Plant Mitigation	\$596K	N/A	4/9/2025	11/26/2025	12/2035
27	Construction	2Q610	29	R7.3/13.5	Pavement rehabilitation.	\$23.3M	4/20/2022	5/3/2024	11/27/2024	11/2026
28	Construction	0Q820	29	11.6/13.0	Repair Culvert and stabilize the roadway.	\$24.47M	9/10/2021	12/4/2023	10/1/2024	12/2026
29	Construction	0Q830	29	46.1	Construct CIDH segmented pile wall at slipout	\$1.7M	6/29/2022	1/22/2024	7/12/2024	03/20/2026
30(Not mapped)	Construction	3Q760	29	Var	Construct rumble strips at seven locations.	\$3.3M	12/31/2021	6/26/2023	3/27/2024	12/31/2024
31	Construction	0K630	29	16.48/19.04	Upgrade / Replace Bridge Rails	\$4.7M	10/22/2020	12/5/2022	7/14/2023	11/2025
32	Construction	0Q810	121	16.0/16.1	Repair pavement, replace drainage systems and upgrade guardrail.	\$1.3M	2/2/2022	6/26/2023	1/23/2024	12/2/2024
33	Construction	4J410	29	1.7/5.1	Rehabilitate Culverts	\$3.3M	2/4/2020	10/3/2022	4/7/2023	11/2025
34	Construction	0Q690	12	2.1/2.6	Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair	\$1.2M	12/1/2020	6/24/2022	3/3/2023	10/30/2024
35	Construction	1G43A	128	R7.4	Environmental mitigation, monitoring and report at Conn Creek	\$0.2M	10/5/2015	8/23/2021	7/26/2022	10/2031
36	Construction	28120	29	5.45/R6.7	Construct New Interchange at SR 221/29/12	\$36.7M	2/13/2020	8/26/2021	5/13/2022	11/2026
37	Construction	2Q260	29	29.24/35.34	Construct Class 1 Multiuse Path	13.2M	11/6/2020	12/10/2021	6/15/2022	10/2025
38	Construction	3G64A	29	37.0	Environmental mitigation at Napa River Bridge	\$0.5M	2/9/2015	5/29/2019	5/28/2020	12/2028

**Caltrans District 4 Active Projects in Napa County - May 2026**

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
<b>39</b>	Construction	4G210	121	0.75	Remove existing triple box culverts and replace with a new single span bridge	\$8.7M	4/9/2018	12/8/2020	6/10/2021	4/30/2024
<b>40</b>	Construction	4G21A	121	0.75	Environmental mitigation, monitoring and report at Huichica Creek	\$1M	4/9/2018	6/9/2023	12/20/2023	6/30/2033
<b>41</b>	Construction	4G84A	128	20.2	Environmental Permit Mitigation & Plant Establishment to Bridge Replacement	\$0.5M	6/16/2016	5/23/2022	12/21/2022	11/17/2031
